

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg/RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
State: Active				8/1/16	8/17/22											
Phase: 0A				8/1/19	1/7/20											
Project Name: AV Portables				8/1/19	1/7/20											
Construction	AV Portables	ALL Mickey Kim	0A	8/1/19	1/7/20											
Phase: 0FA				12/10/18	11/24/20											
Project Name: Fire Alarms/Life Safety Sys				12/10/18	11/25/19											
Construction	Fire Alarms/Life Safety Sys - Phase IV	All Artin Mgrtichian	OFA	12/10/18	11/25/19											
Project Name: Fire Alarms/Life Safety Sys				12/4/19	11/24/20											
Construction	Fire Alarms/Life Safety Sys - Phase V	All Artin Mgrtichian	OFA	12/4/19	11/24/20											
Phase: 0ICS				8/1/16	12/27/19											
Project Name: ICS				8/1/16	12/27/19											
Construction	ICS	ALL Mickey Kim	0ICS	8/1/16	12/27/19											
Phase: 0S				8/22/18	10/23/19											
Project Name: Security Improvements				8/22/18	10/23/19											
Construction	Security Improvements	ALL Mickey Kim	0S	8/22/18	10/23/19											
Phase: 1				9/6/16	12/30/19											
Project Name: Jordan HS Ph 1C, 1D & 4				10/18/17	12/30/19											
Construction	Jordan HS Ph 1C, 1D & 4	A Jason King	1	10/18/17	12/9/19											
Owner Move-in Phase 1C	Jordan HS Ph 1C, 1D & 4	A Jason King	1	8/1/19	8/14/19											
Owner Move-in Phase 4	Jordan HS Ph 1C, 1D & 4	A Jason King	1	12/10/19	12/30/19											
Project Name: Renaissance HS				9/6/16	1/4/19											
Construction	Renaissance HS	E Dan Barr	1	9/6/16	1/4/19											
Owner Move-in	Renaissance HS	E Dan Barr	1	7/16/18	7/16/18											
Phase: 2				12/20/17	8/14/20											
Project Name: Kettering ES HVAC				2/5/18	10/28/19											
Construction - Classroom Buildings	Kettering ES HVAC	F Jacob Keaton	2	2/5/18	8/14/18											
Owner Move-in - Phase 1	Kettering ES HVAC	F Jacob Keaton	2	6/16/18	6/22/18											
Construction - Site Work	Kettering ES HVAC	F Jacob Keaton	2	8/15/18	11/14/18											
Owner Move-in - Phase 2	Kettering ES HVAC	F Jacob Keaton	2	8/18/18	8/30/18											
Construction - Security Fencing & Vestibule	Kettering ES HVAC	F Jacob Keaton	2	3/1/19	10/28/19											
Project Name: Poly HS Track/Field				12/20/17	9/10/18											
Construction	Poly HS Track/Field	E Dan Barr	2	12/20/17	9/10/18											
Owner Move-in	Poly HS Track/Field	E Dan Barr	2	9/10/18	9/10/18											
Project Name: Rogers MS HVAC				2/12/18	8/14/20											

Project updates
Date: 9/11/19

Task Summary

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg/RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Construction	Rogers MS HVAC	F Jacob Keaton	2	2/12/18	8/14/18											
Owner Move-in	Rogers MS HVAC	F Jacob Keaton	2	8/15/18	8/27/18											
Construction - Locker Room	Rogers MS HVAC	F Jacob Keaton	2	6/20/20	8/14/20											
Project Name: Rogers MS Track/Field				6/18/18	8/27/18											
Construction	Rogers MS Track/Field	F Jacob Keaton	2	6/18/18	8/24/18											
Owner Move-in	Rogers MS Track/Field	F Jacob Keaton	2	8/27/18	8/27/18											
Phase: 3				6/11/18	8/28/20											
Project Name: Barton ES HVAC				6/18/18	8/13/19											
Construction - Phase 1	Barton ES HVAC	A Jason King	3	6/18/18	12/21/18											
Owner Move-in Phase 1	Barton ES HVAC	A Jason King	3	12/31/18	1/2/19											
Construction - Phase 2	Barton ES HVAC	A Jason King	3	1/3/19	6/19/19											
Owner Move-in Phase 2	Barton ES HVAC	A Jason King	3	6/19/19	6/21/19											
Construction - Phase 3	Barton ES HVAC	A Jason King	3	6/22/19	8/6/19											
Owner Move-in Phase 3	Barton ES HVAC	A Jason King	3	8/7/19	8/13/19											
Project Name: Burcham ES HVAC				6/25/18	9/27/19											
Construction	Burcham ES HVAC	C Tari Fowler	3	6/25/18	9/25/19											
Owner Move-in - Phase 1	Burcham ES HVAC	C Tari Fowler	3	1/2/19	1/18/19											
Owner Move-in - Phase 2	Burcham ES HVAC	C Tari Fowler	3	7/29/19	7/31/19											
Owner Move-in - Phase 3	Burcham ES HVAC	C Tari Fowler	3	9/26/19	9/27/19											
Project Name: Jefferson MS HVAC				9/10/18	11/25/19											
Construction	Jefferson MS HVAC	F Jacob Keaton	3	9/10/18	8/26/19											
Construction - elevator	Jefferson MS HVAC	F Jacob Keaton	3	5/1/19	11/25/19											
Owner Move-in	Jefferson MS HVAC	F Jacob Keaton	3	8/22/19	8/26/19											
Project Name: Jefferson MS Track/Field				12/1/18	8/25/19											
Construction	Jefferson MS Track/Field	F Jacob Keaton	3	12/1/18	8/25/19											
Owner Move-in	Jefferson MS Track/Field	F Jacob Keaton	3	8/21/19	8/25/19											
Project Name: Jordan HS Ph 2A (Bldgs 10)				10/25/18	10/22/19											
Construction	Jordan HS Ph 2A (Bldgs 100/400)	A Jason King	3	10/25/18	10/8/19											
Owner Move-in	Jordan HS Ph 2A (Bldgs 100/400)	A Jason King	3	10/9/19	10/22/19											
Project Name: Keller MS Conversion				9/12/18	4/26/19											

Project updates
Date: 9/11/19





This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg/RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Construction	Keller MS Conversion	C Tari Fowler	3	9/12/18	4/25/19											
Owner Move-in - Phase 1	Keller MS Conversion	C Tari Fowler	3	4/25/19	4/26/19											
Project Name: Keller MS HVAC				9/12/18	8/22/19											
Construction	Keller MS HVAC	C Tari Fowler	3	9/12/18	8/19/19											
Owner Move-in - Phase 1	Keller MS HVAC	C Tari Fowler	3	4/25/19	4/28/19											
Owner Move-in - Phase 2	Keller MS HVAC	C Tari Fowler	3	8/20/19	8/22/19											
Project Name: Lakewood HS HVAC				6/25/18	8/27/20											
Construction - Bldg 200	Lakewood HS HVAC	B Jason King	3	6/25/18	11/16/18											
Construction - Bldgs 300 & 900	Lakewood HS HVAC	B Jason King	3	11/26/18	7/28/19											
Construction - Bldgs 100 & 800, Cafeteria	Lakewood HS HVAC	B Jason King	3	6/17/19	8/16/19											
Construction - Bldgs 400 & 800	Lakewood HS HVAC	B Jason King	3	8/5/19	12/20/19											
Construction - Bldgs 500 & 800 (1 & 3 floors)	Lakewood HS HVAC	B Jason King	3	8/16/19	10/21/19											
Owner Move-in - Phase 1	Lakewood HS HVAC	B Jason King	3	8/17/19	8/27/19											
Construction - Bldg 700	Lakewood HS HVAC	B Jason King	3	10/22/19	2/24/20											
Owner Move-in - Phase 2	Lakewood HS HVAC	B Jason King	3	2/25/20	3/9/20											
Construction - Gym bldg and portables FA	Lakewood HS HVAC	B Jason King	3	3/1/20	8/20/20											
Owner Move-in - Phase 3	Lakewood HS HVAC	B Jason King	3	8/21/20	8/27/20											
Project Name: Lindsey MS HVAC (Bldg D)				6/18/18	1/2/19											
Construction	Lindsey MS HVAC (Bldg D)	A Jason King	3	6/18/18	12/21/18											
Owner Move-in	Lindsey MS HVAC (Bldg D)	A Jason King	3	1/2/19	1/2/19											
Project Name: Longfellow ES HVAC				6/18/18	8/28/20											
Construction - Auditorium	Longfellow ES HVAC	E Dan Barr	3	6/18/18	8/11/18											
Construction - CR Bldgs 1000 & 2000	Longfellow ES HVAC	E Dan Barr	3	7/2/18	4/26/19											
Owner Move-In - Auditorium	Longfellow ES HVAC	E Dan Barr	3	8/12/18	8/16/18											
Construction - CR Bldgs 3000 & 4000	Longfellow ES HVAC	E Dan Barr	3	4/22/19	8/13/19											
Construction - Kindergarten Rooms	Longfellow ES HVAC	E Dan Barr	3	4/22/19	10/29/19											
Owner Move-in - CR Bldgs 1000 & 2000	Longfellow ES HVAC	E Dan Barr	3	4/24/19	4/28/19											

Project updates
Date: 9/11/19

Task  Summary 

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg/RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Owner Move-in - CR Bldgs 3000 & 4000	Longfellow ES HVAC	E Dan Barr	3	8/14/19	8/18/19											
Construction - Kitchen	Longfellow ES HVAC	E Dan Barr	3	6/18/20	8/24/20											
Owner Move-in - Kitchen	Longfellow ES HVAC	E Dan Barr	3	8/25/20	8/28/20											
Project Name: Lowell ES HVAC				9/10/18	8/25/19											
Construction	Lowell ES HVAC	F Jacob Keaton	3	9/10/18	8/25/19											
Owner Move-in (Classrooms building)	Lowell ES HVAC	F Jacob Keaton	3	6/14/19	6/20/19											
Owner Move-in (Non-Classrooms)	Lowell ES HVAC	F Jacob Keaton	3	8/21/19	8/25/19											
Project Name: MacArthur ES HVAC				6/25/18	8/21/19											
Construction - Bldgs B & C	MacArthur ES HVAC	B Jason King	3	6/25/18	1/2/19											
Construction - Bldg A	MacArthur ES HVAC	B Jason King	3	12/24/18	4/19/19											
Owner Move-in Bldgs B & C	MacArthur ES HVAC	B Jason King	3	1/2/19	1/4/19											
Owner Move-in Bldg A	MacArthur ES HVAC	B Jason King	3	4/20/19	4/23/19											
Construction - Bldg D	MacArthur ES HVAC	B Jason King	3	4/24/19	8/16/19											
Construction - Bldg E	MacArthur ES HVAC	B Jason King	3	6/13/19	8/19/19											
Owner Move-in Bldgs D & E	MacArthur ES HVAC	B Jason King	3	8/17/19	8/21/19											
Project Name: Mann ES HVAC				9/4/18	8/19/19											
Construction	Mann ES HVAC	F Jacob Keaton	3	9/4/18	8/18/19											
Owner Move-in - Phase 1	Mann ES HVAC	F Jacob Keaton	3	4/19/19	4/24/19											
Owner Move-in - Phase 2	Mann ES HVAC	F Jacob Keaton	3	8/17/19	8/19/19											
Project Name: McKinley ES HVAC				6/18/18	7/3/19											
Construction Phase 1	McKinley ES HVAC	A Jason King	3	6/18/18	12/21/18											
Owner Move-in Phase 1	McKinley ES HVAC	A Jason King	3	12/26/18	12/27/18											
Construction Phase 2	McKinley ES HVAC	A Jason King	3	12/28/18	7/1/19											
Owner Move-in Phase 2	McKinley ES HVAC	A Jason King	3	7/1/19	7/3/19											
Project Name: Millikan HS New 1000 Bldg				12/3/18	8/3/20											
Construction	Millikan HS New 1000 Bldg	C Tari Fowler	3	12/3/18	7/13/20											
Owner Move-in	Millikan HS New 1000 Bldg	C Tari Fowler	3	7/14/20	8/3/20											
Project Name: Poly HS Bleachers and Field				12/21/18	9/5/19											
Construction - Soil Remediation	Poly HS Bleachers and Field Lighting	E Dan Barr	3	12/21/18	1/4/19											

Project updates
Date: 9/11/19





This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Construction	Poly HS Bleachers and Field Lighting	E	Dan Barr	3	1/22/19	9/5/19											
Project Name: Sato HS New Bldg						6/11/18	8/19/19										
Construction	Sato HS New Bldg	F	Jacob Keaton	3	6/11/18	8/12/19											
Owner Move-in	Sato HS New Bldg	F	Jacob Keaton	3	8/13/19	8/19/19											
Project Name: Webster ES HVAC						8/27/18	8/20/19										
Construction - Phase 1	Webster ES HVAC	D	Tari Fowler	3	8/27/18	5/31/19											
Construction - Auditorium	Webster ES HVAC	D	Tari Fowler	3	4/22/19	8/16/19											
Construction - Cafeteria/Kitchen	Webster ES HVAC	D	Tari Fowler	3	6/15/19	8/20/19											
Owner Move-in Phase 1	Webster ES HVAC	D	Tari Fowler	3	6/17/19	6/27/19											
Owner Move-in Auditorium/Café/Kitchen	Webster ES HVAC	D	Tari Fowler	3	8/17/19	8/18/19											
Phase: 4						6/14/19	7/1/22										
Project Name: Alvarado ES HVAC						7/22/19	7/24/20										
Construction	Alvarado ES HVAC	E	Dan Barr	4	7/22/19	7/10/20											
Owner Move-in	Alvarado ES HVAC	E	Dan Barr	4	7/13/20	7/24/20											
Project Name: Bixby ES HVAC						6/14/19	7/9/20										
Construction	Bixby ES HVAC	F	Jacob Keaton	4	6/14/19	7/2/20											
Owner Move-in - Phase 1	Bixby ES HVAC	F	Jacob Keaton	4	12/21/19	1/6/20											
Owner Move-in - Phase 2	Bixby ES HVAC	F	Jacob Keaton	4	4/10/20	4/14/20											
Owner Move-in Phase 3	Bixby ES HVAC	F	Jacob Keaton	4	7/3/20	7/9/20											
Project Name: Hughes MS Portables						6/20/19	8/28/20										
Construction - AC Paving	Hughes MS Portables	E	Ferdows Fazeli	4	6/20/19	8/22/19											
Construction - Portable Installation	Hughes MS Portables	E	Ferdows Fazeli	4	12/23/19	1/6/20											
Construction - Electrical and Low Voltage work	Hughes MS Portables	E	Ferdows Fazeli	4	6/15/20	8/21/20											
Owner Move-in	Hughes MS Portables	E	Ferdows Fazeli	4	8/24/20	8/28/20											
Project Name: Jordan HS Ph 2B & 3 (Bldg						8/5/20	7/1/22										
Construction - 2B (Bldg 200/300)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	A	Tracy Nishihira	4	8/5/20	4/6/22											
Construction - 3 (Bldg 1000)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	A	Tracy Nishihira	4	7/5/21	3/22/22											
Owner Move-in - 2B (Bldg 200/300)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	A	Tracy Nishihira	4	6/20/22	7/1/22											
Owner Move-in - 3 (Bldg 1000)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	A	Tracy Nishihira	4	6/20/22	7/1/22											
Project Name: Millikan HS Track/Field						1/2/20	8/13/20										

Project updates
Date: 9/11/19

Task  Summary 

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg/RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Construction	Millikan HS Track/Field	C Elston Soares	4	1/2/20	8/12/20											
Owner Move-in	Millikan HS Track/Field	C Elston Soares	4	8/13/20	8/13/20											
Project Name: Muir K8 HVAC				8/19/19	10/1/20											
Construction - Bldgs B & C	Muir K8 HVAC	D Elston Soares	4	8/19/19	1/24/20											
Owner Move-in - Bldgs B & C	Muir K8 HVAC	D Elston Soares	4	1/27/20	2/7/20											
Construction - Bldg A	Muir K8 HVAC	D Elston Soares	4	2/10/20	7/16/20											
Owner Move-in - Bldg A	Muir K8 HVAC	D Elston Soares	4	7/17/20	7/30/20											
Construction - Bldg D	Muir K8 HVAC	D Elston Soares	4	7/31/20	9/17/20											
Owner Move-in - Bldg D	Muir K8 HVAC	D Elston Soares	4	9/18/20	10/1/20											
Project Name: Naples ES Modernization				9/26/19	7/8/20											
Construction	Naples ES Modernization	F Jacquelyn Roberts	4	9/26/19	6/24/20											
Owner Move-in	Naples ES Modernization	F Jacquelyn Roberts	4	6/25/20	7/8/20											
Project Name: Stephens MS Site Improve				8/20/19	1/6/20											
Construction	Stephens MS Site Improvements	D Tari Fowler	4	8/20/19	12/13/19											
Owner Move-in	Stephens MS Site Improvements	D Tari Fowler	4	12/16/19	1/6/20											
Project Name: Stevenson ES Auditorium f				11/18/19	8/28/20											
Construction	Stevenson ES Auditorium Repairs	E Dan Barr	4	11/18/19	8/14/20											
Owner Move-in	Stevenson ES Auditorium Repairs	E Dan Barr	4	8/17/20	8/28/20											
Phase: 5				4/29/20	8/17/22											
Project Name: Cubberly K8 Modernization				6/22/20	7/9/21											
Construction	Cubberly K8 Modernization	C Elston Soares	5	6/22/20	6/25/21											
Owner Move-in	Cubberly K8 Modernization	C Elston Soares	5	6/28/21	7/9/21											
Project Name: Fremont ES HVAC				6/15/20	7/15/21											
Construction	Fremont ES HVAC	F Jacquelyn Roberts	5	6/15/20	7/1/21											
Owner Move-in - Phase 1	Fremont ES HVAC	F Jacquelyn Roberts	5	4/3/21	4/9/21											
Owner Move-in - Phase 2	Fremont ES HVAC	F Jacquelyn Roberts	5	7/2/21	7/15/21											
Project Name: Lakewood HS Track/Field				4/29/20	1/27/21											
Construction	Lakewood HS Track/Field	B Tracy Nishihira	5	4/29/20	12/30/20											
Owner Move-in	Lakewood HS Track/Field	B Tracy Nishihira	5	12/31/20	1/27/21											
Project Name: Madison ES HVAC				6/22/20	7/8/21											
Construction - Phase 1	Madison ES HVAC	B Tracy Nishihira	5	6/22/20	12/28/20											

Project updates
Date: 9/11/19

Task Summary

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg/RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Owner Move-in - Phase 1	Madison ES HVAC	B Tracy Nishihira	5	12/29/20	1/10/21											
Construction - Phase 2	Madison ES HVAC	B Tracy Nishihira	5	1/11/21	6/24/21											
Owner Move-in - Phase 2	Madison ES HVAC	B Tracy Nishihira	5	6/25/21	7/8/21											
Project Name: Prisk ES Modernization				6/29/20	12/30/21											
Construction - Bldg D	Prisk ES Modernization	C Elston Soares	5	6/29/20	8/21/20											
Construction - Bldg B	Prisk ES Modernization	C Elston Soares	5	6/29/20	12/18/20											
Owner Move-in - Bldg D	Prisk ES Modernization	C Elston Soares	5	8/24/20	8/28/20											
Owner Move-in - Bldg B	Prisk ES Modernization	C Elston Soares	5	12/21/20	1/1/21											
Construction - Bldg C	Prisk ES Modernization	C Elston Soares	5	1/2/21	6/18/21											
Owner Move-in - Bldg C	Prisk ES Modernization	C Elston Soares	5	6/21/21	7/2/21											
Construction - Bldg A	Prisk ES Modernization	C Elston Soares	5	7/5/21	12/17/21											
Owner Move-in - Bldg A	Prisk ES Modernization	C Elston Soares	5	12/20/21	12/30/21											
Project Name: Robinson K8 HVAC				6/5/20	6/17/21											
Construction	Robinson K8 HVAC	E Ferdows Fazeli	5	6/5/20	6/10/21											
Owner Move-in	Robinson K8 HVAC	E Ferdows Fazeli	5	6/11/21	6/17/21											
Project Name: Wilson HS HVAC				6/17/20	8/17/22											
Construction	Wilson HS HVAC	F Jacquelyn Roberts	5	6/17/20	7/18/22											
Owner Move-in	Wilson HS HVAC	F Jacquelyn Roberts	5	7/19/22	8/17/22											
State: Complete				10/1/14	5/28/19											
Phase: OFA				6/30/16	9/14/18											
Project Name: Fire Alarms/Life Safety Sys				6/30/16	6/30/17											
Construction	Fire Alarms/Life Safety Sys - Phase II	All Alex Main	OFA	6/30/16	6/30/17											
Project Name: Fire Alarms/Life Safety Sys				7/20/17	9/14/18											
Construction - Monroe	Fire Alarms/Life Safety Sys - Phase III	All Artin Mgrtichian	OFA	7/20/17	12/31/17											
Construction - Marshall	Fire Alarms/Life Safety Sys - Phase III	All Artin Mgrtichian	OFA	9/1/17	9/14/18											
Construction - Cubberly/King	Fire Alarms/Life Safety Sys - Phase III	All Artin Mgrtichian	OFA	9/1/17	9/14/18											
Phase: OSC				7/6/17	1/30/18											
Project Name: Security Camera Phase II				7/6/17	1/30/18											
Construction	Security Camera Phase II	ALL Mickey Kim	OSC	7/6/17	1/30/18											
Phase: OW				9/22/17	8/31/18											
Project Name: E Rate 2016 / 2017				9/22/17	8/31/18											

Project updates
Date: 9/11/19

Task Summary

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg/RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Construction	E Rate 2016 / 2017	ALL Mickey Kim	OW	9/22/17	8/31/18											
Project Name: Wireless Phase V					1/4/18	4/4/18										
Construction	Wireless Phase V	ALL Mickey Kim	OW	1/4/18	4/4/18											
Phase: 1					10/1/14	5/28/19										
Project Name: Barton/Educare ES					2/24/17	7/3/18										
Construction	Barton/Educare ES	A Raymond Esparza	1	2/24/17	5/17/18											
Owner Move-in	Barton/Educare ES	A Raymond Esparza	1	7/2/18	7/3/18											
Project Name: Browning HS New Constru					10/1/14	5/28/19										
Construction	Browning HS New Construction	F Jacob Keaton	1	10/1/14	12/28/17											
Owner Move-in	Browning HS New Construction	F Jacob Keaton	1	7/31/17	1/11/18											
Additional Construction - Site and off-site Work	Browning HS New Construction	F Jacob Keaton	1	12/29/17	5/28/19											
Project Name: Cabrillo HS Track/Field					6/15/17	11/28/17										
Construction	Cabrillo HS Track/Field	D James Warmuth	1	6/15/17	10/26/17											
Owner Move-in	Cabrillo HS Track/Field	D James Warmuth	1	11/14/17	11/28/17											
Project Name: Head Start at Bethune					3/8/18	5/14/18										
Construction	Head Start at Bethune	D James Warmuth	1	3/8/18	5/4/18											
Owner Move-in	Head Start at Bethune	D James Warmuth	1	5/8/18	5/14/18											
Project Name: Head Start at Hudson					10/23/17	4/12/18										
Construction	Head Start at Hudson	D James Warmuth	1	10/23/17	4/11/18											
Owner Move-in	Head Start at Hudson	D James Warmuth	1	4/12/18	4/12/18											
Project Name: Head Start at Jordan Plus					10/24/17	5/8/18										
Construction	Head Start at Jordan Plus	A James Warmuth	1	10/24/17	5/7/18											
Owner Move-in	Head Start at Jordan Plus	A James Warmuth	1	5/8/18	5/8/18											
Project Name: Kettering ES Interim Housi					10/19/17	2/20/18										
Construction	Kettering ES Interim Housing	F Jacob Keaton	1	10/19/17	2/20/18											
Owner Move-in	Kettering ES Interim Housing	F Jacob Keaton	1	12/16/17	1/3/18											
Project Name: Monroe K8 Interim Housin					7/21/17	12/26/17										
Construction	Monroe K8 Interim Housing	B Raymond Esparza	1	7/21/17	12/11/17											
Owner Move-in	Monroe K8 Interim Housing	B Raymond Esparza	1	12/22/17	12/26/17											
Project Name: Poly HS ADA Improvem					6/19/17	9/28/18										
Construction	Poly HS ADA Improvements	E Dan Barr	1	6/19/17	9/28/18											

Project updates
Date: 9/11/19

Task  Summary 

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg/RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Project Name: Poly HS Auditorium						Project Name: Poly HS Auditorium										
Construction	Poly HS Auditorium	E Dan Barr	1	1/6/15	11/2/17											
Owner Move-in	Poly HS Auditorium	E Dan Barr	1	10/23/17	11/2/17											
Project Name: Poly HS Band Bldg Conver:						Project Name: Poly HS Band Bldg Conversion Work										
Construction	Poly HS Band Bldg Conversion Work	E Dan Barr	1	10/23/17	11/14/17											
Owner Move-in	Poly HS Band Bldg Conversion Work	E Dan Barr	1	11/15/17	11/16/17											
Project Name: Riley ES Interim Housing						Project Name: Riley ES Interim Housing										
Construction	Riley ES Interim Housing	B Raymond Esparza	1	10/20/17	12/28/17											
Owner Move-in	Riley ES Interim Housing	B Raymond Esparza	1	12/27/17	12/28/17											
Project Name: Rogers MS Portables						Project Name: Rogers MS Portables										
Construction	Rogers MS Portables	F Richard Camacho	1	10/16/17	12/7/17											
Owner Move-in	Rogers MS Portables	F Richard Camacho	1	12/29/17	12/31/17											
Project Name: Sato HS Conversion						Project Name: Sato HS Conversion										
Construction	Sato HS Conversion	F Richard Camacho	1	6/5/17	9/8/17											
Owner Move-in	Sato HS Conversion	F Richard Camacho	1	8/1/17	8/18/17											
Project Name: Sato HS Gym						Project Name: Sato HS Gym										
Construction	Sato HS Gym	F Richard Camacho	1	5/23/16	1/31/18											
Owner Move-in	Sato HS Gym	F Richard Camacho	1	8/21/17	1/8/18											
Project Name: Wilson HS Auditorium						Project Name: Wilson HS Auditorium										
Construction	Wilson HS Auditorium	F Richard Camacho	1	2/22/16	3/6/18											
Owner Move-in	Wilson HS Auditorium	F Richard Camacho	1	2/21/18	3/6/18											
Project Name: Wilson HS Track/Field						Project Name: Wilson HS Track/Field										
Construction	Wilson HS Track/Field	F Jacob Keaton	1	9/18/17	4/9/18											
Owner Move-in	Wilson HS Track/Field	F Jacob Keaton	1	4/3/18	4/9/18											
Phase: 2						Phase: 2										
Project Name: Cleveland ES HVAC						Project Name: Cleveland ES HVAC										
Construction	Cleveland ES HVAC	B Jacob Keaton	2	1/3/18	8/23/18											
Owner Move-in	Cleveland ES HVAC	B Jacob Keaton	2	8/21/18	8/23/18											
Project Name: Garfield ES HVAC						Project Name: Garfield ES HVAC										
Construction - Phase 1 (Site, Bldgs C & E)	Garfield ES HVAC	D Raymond Esparza	2	2/6/18	7/13/18											
Construction - Phase 2 (Bldgs A, D, & F)	Garfield ES HVAC	D Raymond Esparza	2	7/16/18	8/24/18											


Project updates
Date: 9/11/19

Task Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.

**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 5 projects) as of 7/31/2019**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Owner Move-in - Phase 1	Garfield ES HVAC	D	Raymond Esparza	2	8/13/18	8/18/18											
Owner Move-in - Phase 2	Garfield ES HVAC	D	Raymond Esparza	2	8/20/18	8/28/18											
Construction - Phase 3	Garfield ES HVAC	D	Raymond Esparza	2	8/27/18	11/16/18											
Owner Move-in - Phase 3	Garfield ES HVAC	D	Raymond Esparza	2	10/20/18	10/20/18											
Project Name: Riley ES HVAC					1/3/18	12/23/18											
Construction - Classroom Building	Riley ES HVAC	B	Jacob Keaton	2	1/3/18	8/10/18											
Construction - Site Work	Riley ES HVAC	B	Jacob Keaton	2	8/11/18	12/23/18											
Owner Move-in	Riley ES HVAC	B	Jacob Keaton	2	8/14/18	8/20/18											
Project Name: Stephens MS HVAC					2/9/18	8/30/18											
Construction	Stephens MS HVAC	D	Raymond Esparza	2	2/9/18	8/17/18											
Owner Move-in (furniture)	Stephens MS HVAC	D	Raymond Esparza	2	7/23/18	8/30/18											
Owner Move-in - final	Stephens MS HVAC	D	Raymond Esparza	2	8/13/18	8/18/18											
Project Name: Stephens MS Track/Field					4/16/18	9/18/18											
Construction	Stephens MS Track/Field	D	Raymond Esparza	2	4/16/18	9/17/18											
Owner Move-in	Stephens MS Track/Field	D	Raymond Esparza	2	9/18/18	9/18/18											
Project Name: Webster ES Interim Housing					1/3/18	8/11/18											
Construction	Webster ES Interim Housing	D	Raymond Esparza	2	1/3/18	7/30/18											
Owner Move-in	Webster ES Interim Housing	D	Raymond Esparza	2	7/31/18	8/11/18											

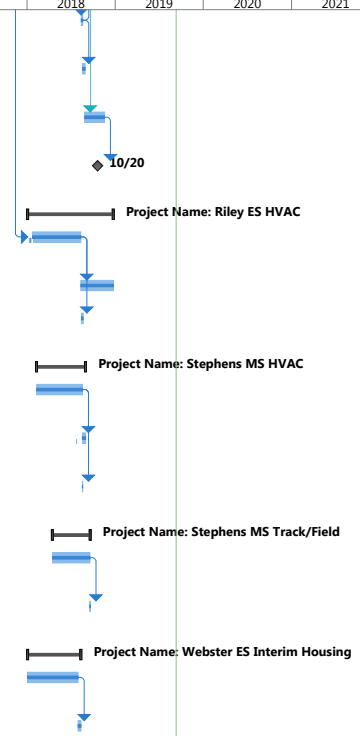

Project updates
Date: 9/11/19

Task Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.
