



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE as of 5/31/2018**

Task Name	Project Name	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half	
<b>State: Active</b>				<b>10/1/14</b>	<b>8/26/26</b>					<b>State: Active</b>
<b>Phase: 0FA</b>				<b>7/20/17</b>	<b>7/22/19</b>					
<b>Project Name: Fire Alarms/Life Safety Sys - Phase III</b>				<b>7/20/17</b>	<b>8/31/18</b>					
Construction - Monroe	Fire Alarms/Life Safety Sys - Phase III		OFA	7/20/17	12/31/17					
Construction - Marshall/Burcham	Fire Alarms/Life Safety Sys - Phase III	Alex Main	OFA	9/1/17	8/31/18					
Construction - Cubberly/King/MacArthur	Fire Alarms/Life Safety Sys - Phase III	Alex Main	OFA	9/1/17	8/31/18					
<b>Project Name: Fire Alarms/Life Safety Sys - Phase IV</b>				<b>7/19/18</b>	<b>7/22/19</b>					
Construction	Fire Alarms/Life Safety Sys - Phase IV	Alex Main	OFA	7/19/18	7/22/19					
<b>Phase: 0ICS</b>				<b>8/1/16</b>	<b>12/18/19</b>					
<b>Project Name: ICS</b>				<b>8/1/16</b>	<b>12/18/19</b>					
Construction	ICS	Mickey Kim	OICS	8/1/16	12/18/19					
<b>Phase: 0W</b>				<b>9/22/17</b>	<b>10/4/18</b>					
<b>Project Name: E Rate 2016 / 2017</b>				<b>9/22/17</b>	<b>5/31/18</b>					
Construction	E Rate 2016 / 2017	Mickey Kim	OW	9/22/17	5/31/18					
<b>Project Name: E Rate 2018 / 2019</b>				<b>7/2/18</b>	<b>10/4/18</b>					
Construction	E Rate 2018 / 2019	Mickey Kim	OW	7/2/18	10/4/18					
<b>Project Name: Wireless Phase V</b>				<b>1/4/18</b>	<b>4/4/18</b>					
Construction	Wireless Phase V	Mickey Kim	OW	1/4/18	4/4/18					
<b>Phase: 1</b>				<b>10/1/14</b>	<b>7/8/19</b>					
<b>Project Name: Barton/Educare ES</b>				<b>2/24/17</b>	<b>7/3/18</b>					
Construction	Barton/Educare ES	Raymond Esparza	1	2/24/17	5/17/18					
Owner Move-in	Barton/Educare ES	Raymond Esparza	1	7/2/18	7/3/18					
<b>Project Name: Browning HS New Construction</b>				<b>10/1/14</b>	<b>6/29/18</b>					
Construction	Browning HS New Construction	Richard Camacho	1	10/1/14	12/28/17					
Owner Move-in	Browning HS New Construction	Richard Camacho	1	7/31/17	1/11/18					
Additional Construction - Site and off-site Work	Browning HS New Construction	Richard Camacho	1	12/29/17	6/29/18					
<b>Project Name: Head Start at Bethune</b>				<b>3/8/18</b>	<b>5/14/18</b>					
Construction	Head Start at Bethune	James Warmuth	1	3/8/18	5/6/18					
Owner Move-in	Head Start at Bethune	James Warmuth	1	5/8/18	5/14/18					
<b>Project Name: Head Start at Hudson</b>				<b>10/23/17</b>	<b>4/12/18</b>					
Construction	Head Start at Hudson	James Warmuth	1	10/23/17	4/11/18					
Owner Move-in	Head Start at Hudson	James Warmuth	1	4/12/18	4/12/18					
<b>Project Name: Head Start at Jordan Plus</b>				<b>10/24/17</b>	<b>5/8/18</b>					
Construction	Head Start at Jordan Plus	James Warmuth	1	10/24/17	5/7/18					
Owner Move-in	Head Start at Jordan Plus	James Warmuth	1	5/8/18	5/8/18					
<b>Project Name: Jordan HS Ph 1C, 1D &amp; 4</b>				<b>10/18/17</b>	<b>7/8/19</b>					
Construction	Jordan HS Ph 1C, 1D & 4	Jason King	1	10/18/17	4/19/19					
Owner Move-in	Jordan HS Ph 1C, 1D & 4	Jason King	1	6/24/19	7/8/19					
<b>Project Name: Kettering ES Interim Housing</b>				<b>10/19/17</b>	<b>2/20/18</b>					
Construction	Kettering ES Interim Housing	Richard Camacho	1	10/19/17	2/20/18					
Owner Move-in	Kettering ES Interim Housing	Richard Camacho	1	12/16/17	1/3/18					
<b>Project Name: Poly HS ADA Improvements</b>				<b>6/19/17</b>	<b>5/31/18</b>					
Construction	Poly HS ADA Improvements	Dan Barr	1	6/19/17	5/31/18					
<b>Project Name: Renaissance HS</b>				<b>9/6/16</b>	<b>7/23/18</b>					
Construction	Renaissance HS	Dan Barr	1	9/6/16	7/6/18					
Owner Move-in	Renaissance HS	Dan Barr	1	7/10/18	7/23/18					
<b>Project Name: Wilson HS Track/Field</b>				<b>9/18/17</b>	<b>4/9/18</b>					
Construction	Wilson HS Track/Field	Richard Camacho	1	9/18/17	3/30/18					
Owner Move-in	Wilson HS Track/Field	Richard Camacho	1	4/3/18	4/9/18					
<b>Phase: 2</b>				<b>12/20/17</b>	<b>12/27/18</b>					
<b>Project Name: Cleveland ES HVAC</b>				<b>1/3/18</b>	<b>8/19/18</b>					
Construction	Cleveland ES HVAC	Raymond Esparza	2	1/3/18	8/13/18					
Owner Move-in	Cleveland ES HVAC	Raymond Esparza	2	8/15/18	8/19/18					
<b>Project Name: Garfield ES HVAC</b>				<b>2/6/18</b>	<b>12/27/18</b>					
Construction - Phase 1 (Site, Bldgs C & E)	Garfield ES HVAC	Raymond Esparza	2	2/6/18	8/10/18					
Construction - Phase 2 (Bldgs A, D, & F)	Garfield ES HVAC	Raymond Esparza	2	6/18/18	8/10/18					
Construction - Phase 3	Garfield ES HVAC	Raymond Esparza	2	6/18/18	11/30/18					
Owner Move-In - Phase 1	Garfield ES HVAC	Raymond Esparza	2	8/13/18	8/19/18					
Owner Move-in - Phase 2	Garfield ES HVAC	Raymond Esparza	2	8/20/18	8/28/18					

Project updates

Task

Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE as of 5/31/2018**

Task Name	Project Name	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
Owner Move-in - Phase 3	Garfield ES HVAC	Raymond Esparza	2	12/22/18	12/27/18				
<b>Project Name: Kettering ES HVAC</b>				<b>2/5/18</b>	<b>11/14/18</b>				
Construction - Classroom Buildings	Kettering ES HVAC	Richard Camacho	2	2/5/18	8/14/18				
Owner Move-in - Phase 1	Kettering ES HVAC	Richard Camacho	2	6/16/18	6/22/18				
Construction - Site Work	Kettering ES HVAC	Richard Camacho	2	8/15/18	11/14/18				
Owner Move-in - Phase 2	Kettering ES HVAC	Richard Camacho	2	8/18/18	8/30/18				
<b>Project Name: Poly HS Track/Field</b>				<b>12/20/17</b>	<b>9/4/18</b>				
Construction	Poly HS Track/Field	Dan Barr	2	12/20/17	8/24/18				
Owner Move-in	Poly HS Track/Field	Dan Barr	2	8/28/18	9/4/18				
<b>Project Name: Riley ES HVAC</b>				<b>1/3/18</b>	<b>12/23/18</b>				
Construction - Classroom Building	Riley ES HVAC	Raymond Esparza	2	1/3/18	8/10/18				
Construction - Site Work	Riley ES HVAC	Raymond Esparza	2	8/11/18	12/23/18				
Owner Move-in	Riley ES HVAC	Raymond Esparza	2	8/11/18	8/14/18				
<b>Project Name: Rogers MS HVAC</b>				<b>2/12/18</b>	<b>8/27/18</b>				
Construction	Rogers MS HVAC	Richard Camacho	2	2/12/18	8/14/18				
Owner Move-in	Rogers MS HVAC	Richard Camacho	2	8/15/18	8/27/18				
<b>Project Name: Rogers MS Track/Field</b>				<b>6/18/18</b>	<b>8/20/18</b>				
Construction	Rogers MS Track/Field	Richard Camacho	2	6/18/18	8/14/18				
Owner Move-in	Rogers MS Track/Field	Richard Camacho	2	8/15/18	8/20/18				
<b>Project Name: Stephens MS HVAC</b>				<b>2/9/18</b>	<b>8/18/18</b>				
Construction	Stephens MS HVAC	Raymond Esparza	2	2/9/18	8/17/18				
Owner Move-in (furniture)	Stephens MS HVAC	Raymond Esparza	2	7/23/18	8/3/18				
Owner Move-in - final	Stephens MS HVAC	Raymond Esparza	2	8/13/18	8/18/18				
<b>Project Name: Stephens MS Track/Field</b>				<b>4/16/18</b>	<b>9/17/18</b>				
Construction	Stephens MS Track/Field	Raymond Esparza	2	4/16/18	8/31/18				
Owner Move-in	Stephens MS Track/Field	Raymond Esparza	2	9/4/18	9/17/18				
<b>Project Name: Webster ES Interim Housing</b>				<b>1/3/18</b>	<b>8/11/18</b>				
Construction	Webster ES Interim Housing	Raymond Esparza	2	1/3/18	7/30/18				
Owner Move-in	Webster ES Interim Housing	Raymond Esparza	2	7/31/18	8/11/18				
<b>Phase: 3</b>				<b>6/11/18</b>	<b>6/26/20</b>				
<b>Project Name: Barton ES HVAC</b>				<b>6/18/18</b>	<b>7/1/19</b>				
Construction - Phase 1	Barton ES HVAC	Jason King	3	6/18/18	12/20/18				
Owner Move-in Phase 1	Barton ES HVAC	Jason King	3	12/21/18	1/3/19				
Construction - Phase 2	Barton ES HVAC	Jason King	3	1/4/19	6/17/19				
Owner Move-in Phase 2	Barton ES HVAC	Jason King	3	6/18/19	7/1/19				
<b>Project Name: Burcham ES HVAC</b>				<b>6/25/18</b>	<b>8/15/19</b>				
Construction	Burcham ES HVAC	Tari Fowler	3	6/25/18	8/15/19				
Owner Move-in - Phase 1	Burcham ES HVAC	Tari Fowler	3	11/17/18	11/18/18				
Owner Move-in - Phase 2	Burcham ES HVAC	Tari Fowler	3	4/20/19	4/26/19				
<b>Project Name: Jefferson MS HVAC</b>				<b>7/10/18</b>	<b>7/15/19</b>				
Construction	Jefferson MS HVAC	Richard Camacho	3	7/10/18	6/28/19				
Owner Move-in	Jefferson MS HVAC	Richard Camacho	3	7/1/19	7/15/19				
<b>Project Name: Jefferson MS Track/Field</b>				<b>7/11/18</b>	<b>2/18/19</b>				
Construction	Jefferson MS Track/Field	Richard Camacho	3	7/11/18	2/4/19				
Owner Move-in	Jefferson MS Track/Field	Richard Camacho	3	2/5/19	2/18/19				
<b>Project Name: Jordan HS Ph 2A (Bldgs 100/400)</b>				<b>9/27/18</b>	<b>8/9/19</b>				
Construction	Jordan HS Ph 2A (Bldgs 100/400)	Jason King	3	9/27/18	7/26/19				
Owner Move-in	Jordan HS Ph 2A (Bldgs 100/400)	Jason King	3	7/29/19	8/9/19				
<b>Project Name: Keller MS Conversion</b>				<b>9/12/18</b>	<b>8/29/19</b>				
Construction	Keller MS Conversion	Leslie Sydnor	3	9/12/18	8/29/19				
Owner Move-in - Phase 1	Keller MS Conversion	Leslie Sydnor	3	2/15/19	2/17/19				
Owner Move-in - Phase 2	Keller MS Conversion	Leslie Sydnor	3	8/17/19	8/23/19				
<b>Project Name: Keller MS Modernization</b>				<b>9/12/18</b>	<b>8/29/19</b>				
Construction	Keller MS Modernization	Leslie Sydnor	3	9/12/18	8/29/19				
Owner Move-in - Phase 1	Keller MS Modernization	Leslie Sydnor	3	2/15/19	2/18/19				
Owner Move-in - Phase 2	Keller MS Modernization	Leslie Sydnor	3	8/17/19	8/23/19				
<b>Project Name: Lakewood HS HVAC</b>				<b>6/14/18</b>	<b>3/24/20</b>				
Construction	Lakewood HS HVAC	James Warmuth	3	6/14/18	3/10/20				
Owner Move-in - Phase 1	Lakewood HS HVAC	James Warmuth	3	7/1/19	7/15/19				
Owner Move-in - Phase 2	Lakewood HS HVAC	James Warmuth	3	3/11/20	3/24/20				

Project updates      Task      Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability. 2



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE as of 5/31/2018**

Task Name	Project Name	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
<b>Project Name: Lindsey MS HVAC (Bldg D)</b>				<b>6/20/18</b>	<b>1/4/19</b>		<b>Project Name: Lindsey MS HVAC (Bldg D)</b>		
Construction	Lindsey MS HVAC (Bldg D)	Jason King	3	6/20/18	12/21/18				
Owner Move-in	Lindsey MS HVAC (Bldg D)	Jason King	3	12/22/18	1/4/19				
<b>Project Name: Longfellow ES HVAC</b>				<b>6/18/18</b>	<b>8/2/19</b>		<b>Project Name: Longfellow ES HVAC</b>		
Construction - Auditorium/Cafeteria/Kitchen	Longfellow ES HVAC	Dan Barr	3	6/18/18	8/2/19				
Construction - Classrooms	Longfellow ES HVAC	Dan Barr	3	7/2/18	6/21/19				
Owner Move-in - Phase 1	Longfellow ES HVAC	Dan Barr	3	12/22/18	12/27/18				
Owner Move-in - Phase 2	Longfellow ES HVAC	Dan Barr	3	6/24/19	7/8/19				
<b>Project Name: Lowell ES HVAC</b>				<b>8/20/18</b>	<b>8/28/19</b>		<b>Project Name: Lowell ES HVAC</b>		
Construction	Lowell ES HVAC	Richard Camacho	3	8/20/18	8/14/19				
Owner Move-in (Classrooms building)	Lowell ES HVAC	Richard Camacho	3	6/14/19	6/20/19				
Owner Move-in (Non-Classrooms)	Lowell ES HVAC	Richard Camacho	3	8/15/19	8/28/19				
<b>Project Name: MacArthur ES HVAC</b>				<b>6/25/18</b>	<b>8/30/19</b>		<b>Project Name: MacArthur ES HVAC</b>		
Construction - Bldgs B & C	MacArthur ES HVAC	James Warmuth	3	6/25/18	11/9/18				
Owner Move-in Bldgs B & C	MacArthur ES HVAC	James Warmuth	3	11/12/18	11/16/18				
Construction - Bldg A	MacArthur ES HVAC	James Warmuth	3	11/17/18	4/19/19				
Owner Move-in Bldg A	MacArthur ES HVAC	James Warmuth	3	4/22/19	4/26/19				
Construction - Bldgs D & E	MacArthur ES HVAC	James Warmuth	3	4/29/19	8/23/19				
Owner Move-in Bldgs D & E	MacArthur ES HVAC	James Warmuth	3	8/26/19	8/30/19				
<b>Project Name: Mann ES HVAC</b>				<b>8/18/18</b>	<b>8/22/19</b>		<b>Project Name: Mann ES HVAC</b>		
Construction	Mann ES HVAC	Richard Camacho	3	8/18/18	8/15/19				
Owner Move-in - Phase 1	Mann ES HVAC	Richard Camacho	3	12/22/18	1/4/19				
Owner Move-in - Phase 2	Mann ES HVAC	Richard Camacho	3	6/18/19	7/1/19				
Owner Move-in - Phase 3	Mann ES HVAC	Richard Camacho	3	8/16/19	8/22/19				
<b>Project Name: McKinley ES HVAC</b>				<b>6/18/18</b>	<b>7/8/19</b>		<b>Project Name: McKinley ES HVAC</b>		
Construction Phase 1	McKinley ES HVAC	Jason King	3	6/18/18	12/20/18				
Owner Move-in Phase 1	McKinley ES HVAC	Jason King	3	12/22/18	1/4/19				
Construction Phase 2	McKinley ES HVAC	Jason King	3	1/7/19	6/21/19				
Owner Move-in Phase 2	McKinley ES HVAC	Jason King	3	6/24/19	7/8/19				
<b>Project Name: Millikan HS New 1000 Bldg</b>				<b>9/17/18</b>	<b>6/26/20</b>		<b>Project Name: Millikan HS New 1000 Bldg</b>		
Construction	Millikan HS New 1000 Bldg	Leslie Sydnor	3	9/17/18	5/27/20				
Owner Move-in	Millikan HS New 1000 Bldg	Leslie Sydnor	3	5/28/20	6/26/20				
<b>Project Name: Poly HS Bleachers and Field Lighting</b>				<b>10/19/18</b>	<b>5/2/19</b>		<b>Project Name: Poly HS Bleachers and Field Lighting</b>		
Construction	Poly HS Bleachers and Field Lighting	Brooke Clements	3	10/19/18	5/2/19				
<b>Project Name: Sato HS New Bldg</b>				<b>6/11/18</b>	<b>6/19/19</b>		<b>Project Name: Sato HS New Bldg</b>		
Construction	Sato HS New Bldg	Richard Camacho	3	6/11/18	6/5/19				
Owner Move-in	Sato HS New Bldg	Richard Camacho	3	6/6/19	6/19/19				
<b>Project Name: Webster ES HVAC</b>				<b>6/25/18</b>	<b>7/2/19</b>		<b>Project Name: Webster ES HVAC</b>		
Construction	Webster ES HVAC	Raymond Esparza	3	6/25/18	6/18/19				
Owner Move-in	Webster ES HVAC	Raymond Esparza	3	6/19/19	7/2/19				
<b>Phase: 4</b>				<b>6/14/19</b>	<b>8/12/21</b>		<b>Phase: 4</b>		
<b>Project Name: Alvarado ES HVAC</b>				<b>6/17/19</b>	<b>7/23/20</b>		<b>Project Name: Alvarado ES HVAC</b>		
Construction	Alvarado ES HVAC	Brooke Clements	4	6/17/19	7/9/20				
Owner Move-in	Alvarado ES HVAC	Brooke Clements	4	7/10/20	7/23/20				
<b>Project Name: Bixby ES HVAC</b>				<b>7/2/19</b>	<b>8/7/20</b>		<b>Project Name: Bixby ES HVAC</b>		
Construction	Bixby ES HVAC	Jacquelyn Roberts	4	7/2/19	7/31/20				
Owner Move-in - Phase 1	Bixby ES HVAC	Jacquelyn Roberts	4	4/11/20	4/17/20				
Owner Move-in - Phase 2	Bixby ES HVAC	Jacquelyn Roberts	4	6/17/20	6/30/20				
Owner Move-in Phase 3	Bixby ES HVAC	Jacquelyn Roberts	4	8/3/20	8/7/20				
<b>Project Name: Cubberly ES Modernization</b>				<b>7/9/19</b>	<b>7/17/20</b>		<b>Project Name: Cubberly ES Modernization</b>		
Construction	Cubberly ES Modernization	Leslie Sydnor	4	7/9/19	7/3/20				
Owner Move-in	Cubberly ES Modernization	Leslie Sydnor	4	7/6/20	7/17/20				
<b>Project Name: Hamilton MS Gym Measure K</b>				<b>6/25/19</b>	<b>7/27/20</b>		<b>Project Name: Hamilton MS Gym Measure K</b>		
Construction	Hamilton MS Gym Measure K	Tracy Nishihira	4	6/25/19	6/26/20				
Owner Move-in	Hamilton MS Gym Measure K	Tracy Nishihira	4	6/29/20	7/27/20				
<b>Project Name: Hamilton MS Track &amp; Field</b>				<b>7/30/19</b>	<b>4/23/20</b>		<b>Project Name: Hamilton MS Track &amp; Field</b>		
Construction	Hamilton MS Track & Field	Tracy Nishihira	4	7/30/19	4/9/20				
Owner Move-in	Hamilton MS Track & Field	Tracy Nishihira	4	4/10/20	4/23/20				
<b>Project Name: Hughes MS HVAC</b>				<b>7/9/19</b>	<b>1/7/21</b>		<b>Project Name: Hughes MS HVAC</b>		
Construction	Hughes MS HVAC	Brooke Clements	4	7/9/19	10/15/20				

Project updates

Task

Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE as of 5/31/2018**

Task Name	Project Name	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
Owner Move-in	Hughes MS HVAC	Brooke Clements	4	12/28/20	1/7/21				
<b>Project Name: Hughes MS Track/Field</b>									<b>Project Name: Hughes MS Track/Field</b>
Construction	Hughes MS Track/Field	Brooke Clements	4	7/9/19	10/15/20				
Owner Move-in	Hughes MS Track/Field	Brooke Clements	4	12/28/20	1/7/21				
<b>Project Name: Jordan HS Ph 2B &amp; 3</b>									<b>Project Name: Jordan HS Ph 2B &amp; 3</b>
Construction - 2B (Bldg 200/300)	Jordan HS Ph 2B & 3	Tracy Nishihira	4	7/29/19	6/18/21				
Construction - 3 (Bldg 1000)	Jordan HS Ph 2B & 3	Tracy Nishihira	4	7/6/20	3/25/21				
Owner Move-in - 3 (Bldg 1000)	Jordan HS Ph 2B & 3	Tracy Nishihira	4	3/26/21	4/1/21				
Owner Move-in - 2B (Bldg 200/300)	Jordan HS Ph 2B & 3	Tracy Nishihira	4	6/21/21	7/2/21				
<b>Project Name: Madison ES HVAC</b>									<b>Project Name: Madison ES HVAC</b>
Construction - non-classroom work	Madison ES HVAC	James Fortunes	4	6/17/19	7/16/20				
Construction - Classrooms	Madison ES HVAC	James Fortunes	4	6/24/19	6/2/20				
Owner Move-in - Phase 1	Madison ES HVAC	James Fortunes	4	4/11/20	4/17/20				
Owner Move-in - Phase 2	Madison ES HVAC	James Fortunes	4	6/3/20	6/16/20				
<b>Project Name: Millikan HS Track/Field</b>									<b>Project Name: Millikan HS Track/Field</b>
Construction	Millikan HS Track/Field	Leslie Sydnor	4	6/19/19	11/29/19				
Owner Move-in	Millikan HS Track/Field	Leslie Sydnor	4	12/2/19	12/13/19				
<b>Project Name: Muir K8 HVAC</b>									<b>Project Name: Muir K8 HVAC</b>
Construction	Muir K8 HVAC	Elston Soares	4	6/26/19	6/25/20				
Owner Move-in	Muir K8 HVAC	Elston Soares	4	6/26/20	7/9/20				
<b>Project Name: Muir K8 Track/Field</b>									<b>Project Name: Muir K8 Track/Field</b>
Construction	Muir K8 Track/Field	Elston Soares	4	6/26/19	1/27/20				
Owner Move-in	Muir K8 Track/Field	Elston Soares	4	1/28/20	2/3/20				
<b>Project Name: Naples ES Modernization</b>									<b>Project Name: Naples ES Modernization</b>
Construction	Naples ES Modernization	Jacquelyn Roberts	4	6/21/19	12/20/19				
Owner Move-in	Naples ES Modernization	Jacquelyn Roberts	4	12/23/19	1/6/20				
<b>Project Name: Prisk ES Modernization</b>									<b>Project Name: Prisk ES Modernization</b>
Construction	Prisk ES Modernization	Leslie Sydnor	4	6/20/19	7/17/20				
Owner Move-in	Prisk ES Modernization	Leslie Sydnor	4	7/20/20	7/31/20				
<b>Project Name: Wilson HS HVAC</b>									<b>Project Name: Wilson HS HVAC</b>
Construction	Wilson HS HVAC	Jacquelyn Roberts	4	6/14/19	7/13/21				
Owner Move-in	Wilson HS HVAC	Jacquelyn Roberts	4	7/14/21	8/12/21				
<b>Phase: 5</b>									<b>Phase: 5</b>
<b>Project Name: Avalon K-12 HVAC</b>									<b>Project Name: Avalon K-12 HVAC</b>
Construction	Avalon K-12 HVAC	Elston Soares	5	6/19/20	6/30/21				
Owner Move-in	Avalon K-12 HVAC	Elston Soares	5	6/17/21	6/30/21				
<b>Project Name: Bancroft MS HVAC</b>									<b>Project Name: Bancroft MS HVAC</b>
Construction	Bancroft MS HVAC	James Fortunes	5	1/8/21	1/20/22				
Owner Move-in	Bancroft MS HVAC	James Fortunes	5	1/7/22	1/20/22				
<b>Project Name: Birney ES Modernization</b>									<b>Project Name: Birney ES Modernization</b>
Construction	Birney ES Modernization	Brooke Clements	5	7/10/20	7/7/21				
Owner Move-in	Birney ES Modernization	Brooke Clements	5	6/24/21	7/7/21				
<b>Project Name: Fremont ES HVAC</b>									<b>Project Name: Fremont ES HVAC</b>
Construction	Fremont ES HVAC	Jacquelyn Roberts	5	7/1/20	6/28/21				
Owner Move-in - Phase 1	Fremont ES HVAC	Jacquelyn Roberts	5	4/3/21	4/9/21				
Owner Move-in - Phase 2	Fremont ES HVAC	Jacquelyn Roberts	5	6/15/21	6/28/21				
<b>Project Name: Holmes ES HVAC</b>									<b>Project Name: Holmes ES HVAC</b>
Construction	Holmes ES HVAC	James Fortunes	5	6/3/20	6/15/21				
Owner Move-in - Phase 1	Holmes ES HVAC	James Fortunes	5	4/3/21	4/9/21				
Owner Move-in - Phase 2	Holmes ES HVAC	James Fortunes	5	6/2/21	6/15/21				
<b>Project Name: Lakewood HS Track/Field</b>									<b>Project Name: Lakewood HS Track/Field</b>
Construction	Lakewood HS Track/Field	James Fortunes	5	5/27/20	1/26/21				
Owner Move-in	Lakewood HS Track/Field	James Fortunes	5	1/27/21	2/24/21				
<b>Project Name: Millikan HS Modernization</b>									<b>Project Name: Millikan HS Modernization</b>
Construction	Millikan HS Modernization	Leslie Sydnor	5	7/9/20	11/11/21				
Owner Move-in	Millikan HS Modernization	Leslie Sydnor	5	11/12/21	11/25/21				
<b>Project Name: Stanford MS HVAC</b>									<b>Project Name: Stanford MS HVAC</b>
Construction	Stanford MS HVAC	Leslie Sydnor	5	8/3/20	7/29/21				
Owner Move-in Phase 1	Stanford MS HVAC	Leslie Sydnor	5	12/21/20	1/1/21				
Owner Move-in Phase 2	Stanford MS HVAC	Leslie Sydnor	5	7/30/21	8/12/21				

Project updates


Task  Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE as of 5/31/2018**

Task Name	Project Name	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
<b>Project Name: Stanford MS Track/Field</b>									
Construction	Stanford MS Track/Field	Leslie Sydnor	5	6/15/20	12/29/20				
Owner Move-in	Stanford MS Track/Field	Leslie Sydnor	5	12/16/20	12/29/20				
<b>Project Name: Twain ES HVAC</b>									
Construction	Twain ES HVAC	James Fortunes	5	7/20/20	7/29/21				
Owner Move-in - Phase 1	Twain ES HVAC	James Fortunes	5	4/3/21	4/9/21				
Owner Move-in - Phase 2	Twain ES HVAC	James Fortunes	5	7/16/21	7/29/21				
<b>Project Name: Washington MS HVAC</b>									
Construction	Washington MS HVAC	Elston Soares	5	6/22/20	6/25/21				
Owner Move-in	Washington MS HVAC	Elston Soares	5	6/14/21	6/25/21				
<b>Phase: 6</b>									
<b>Project Name: Bancroft MS Track/Field</b>									
Construction	Bancroft MS Track/Field	James Fortunes	6	4/28/21	1/11/22				
Owner Move-in	Bancroft MS Track/Field	James Fortunes	6	1/12/22	1/25/22				
<b>Project Name: Beach HS Modernization</b>									
Construction	Beach HS Modernization	Jacquelyn Roberts	6	6/14/21	7/13/22				
Owner Move-in	Beach HS Modernization	Jacquelyn Roberts	6	7/13/22	7/26/22				
<b>Project Name: Bryant ES Modernization</b>									
Construction	Bryant ES Modernization	Jacquelyn Roberts	6	6/29/21	12/29/21				
Owner Move-in	Bryant ES Modernization	Jacquelyn Roberts	6	12/30/21	1/12/22				
<b>Project Name: Emerson ES Modernization</b>									
Construction	Emerson ES Modernization	Leslie Sydnor	6	7/30/21	8/5/22				
Owner Move-in	Emerson ES Modernization	Leslie Sydnor	6	7/25/22	8/5/22				
<b>Project Name: Gant ES Modernization</b>									
Construction (Non Classrooms)	Gant ES Modernization	Jacquelyn Roberts	6	7/30/21	7/22/22				
Owner Move-in	Gant ES Modernization	Jacquelyn Roberts	6	7/25/22	8/5/22				
<b>Project Name: Gompers K8 Modernization</b>									
Construction	Gompers K8 Modernization	James Fortunes	6	6/2/21	6/14/22				
Owner Move-in	Gompers K8 Modernization	James Fortunes	6	6/1/22	6/14/22				
<b>Project Name: Hoover MS HVAC</b>									
Construction	Hoover MS HVAC	James Fortunes	6	1/21/22	2/17/23				
Owner Move-in	Hoover MS HVAC	James Fortunes	6	1/20/23	2/17/23				
<b>Project Name: Jordan HS Ph 5 &amp; 6</b>									
Construction - Gym	Jordan HS Ph 5 & 6	Tracy Nishihira	6	6/21/21	10/6/22				
Construction - Pool, Bleachers, Stadium	Jordan HS Ph 5 & 6	Tracy Nishihira	6	10/19/22	3/1/24				
Owner Move-in - Gym	Jordan HS Ph 5 & 6	Tracy Nishihira	6	3/4/24	3/15/24				
Owner Move-in - Pool, Bleachers, Stadium	Jordan HS Ph 5 & 6	Tracy Nishihira	6	3/4/24	3/15/24				
Construction - Fields	Jordan HS Ph 5 & 6	Tracy Nishihira	6	3/18/24	9/11/24				
<b>Project Name: Lakewood HS Pool/Nat</b>									
Construction	Lakewood HS Pool/Nat	James Fortunes	6	7/9/21	8/11/22				
Owner Move-in	Lakewood HS Pool/Nat	James Fortunes	6	7/29/22	8/11/22				
<b>Project Name: Poly HS Multi-Phase</b>									
Construction	Poly HS Multi-Phase	Brooke Clements	6	7/16/21	8/8/23				
Owner Move-in	Poly HS Multi-Phase	Brooke Clements	6	7/26/23	8/8/23				
<b>Project Name: Sato HS HVAC</b>									
Construction	Sato HS HVAC	Jacquelyn Roberts	6	6/14/21	8/2/22				
Owner Move-in	Sato HS HVAC	Jacquelyn Roberts	6	7/20/22	8/2/22				
<b>Project Name: Washington MS Track/Field</b>									
Construction	Washington MS Track/Field	Elston Soares	6	7/7/21	3/1/22				
Owner Move-in	Washington MS Track/Field	Elston Soares	6	2/16/22	3/1/22				
<b>Phase: 7</b>									
<b>Project Name: Gompers K8 Track/Field</b>									
Construction	Gompers K8 Track/Field	James Fortunes	7	5/20/21	8/25/23				
Owner Move-in	Gompers K8 Track/Field	James Fortunes	7	5/17/22	11/7/22				
Construction	Gompers K8 Track/Field	James Fortunes	7	11/30/22	10/31/22				
Owner Move-in	Gompers K8 Track/Field	James Fortunes	7	11/1/22	11/7/22				
<b>Project Name: Hoover MS Track/Field</b>									
Construction	Hoover MS Track/Field	James Fortunes	7	11/30/22	8/15/23				
Owner Move-in	Hoover MS Track/Field	James Fortunes	7	8/2/23	8/15/23				
<b>Project Name: Los Cerritos ES Modernization</b>									
Construction	Los Cerritos ES Modernization	Brooke Clements	7	6/1/22	5/30/23				
Owner Move-in	Los Cerritos ES Modernization	Brooke Clements	7	6/1/22	5/16/23				

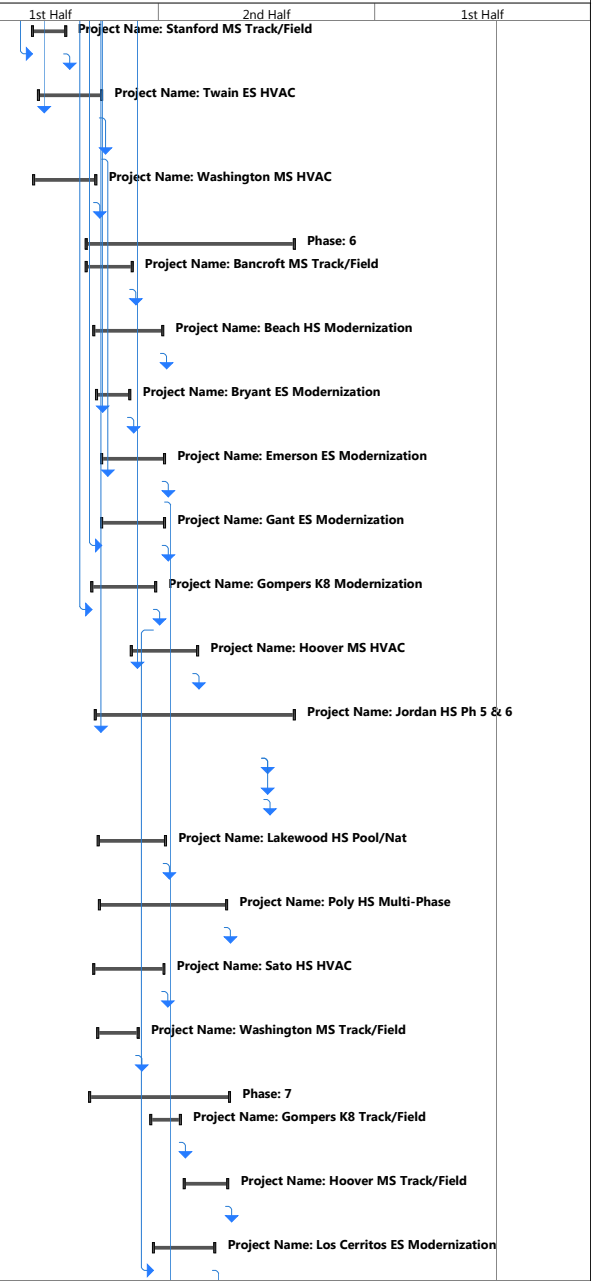

Project updates | Task | Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE as of 5/31/2018**

Task Name	Project Name	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
Owner Move-in	Los Cerritos ES Modernization	Brooke Clements	7	5/17/23	5/30/23				
<b>Project Name: Marshall MS Modernization</b>									
Construction	Marshall MS Modernization	Leslie Sydnor	7	8/17/22	8/9/23				
Owner Move-in	Marshall MS Modernization	Leslie Sydnor	7	8/10/23	8/23/23				
<b>Project Name: Newcomb K8 Track/Field</b>									
Construction	Newcomb K8 Track/Field	Leslie Sydnor	7	3/15/22	11/15/22				
Owner Move-in	Newcomb K8 Track/Field	Leslie Sydnor	7	11/16/22	11/29/22				
<b>Project Name: Sato HS Track/Field</b>									
Construction	Sato HS Track/Field	Jacquelyn Roberts	7	5/20/21	1/19/22				
Owner Move-in	Sato HS Track/Field	Jacquelyn Roberts	7	1/20/22	2/2/22				
<b>Project Name: Tincher K8 Modernization</b>									
Construction	Tincher K8 Modernization	Jacquelyn Roberts	7	8/8/22	8/11/23				
Owner Move-in	Tincher K8 Modernization	Jacquelyn Roberts	7	8/14/23	8/25/23				
<b>Project Name: Wilson HS Pool/Nat</b>									
Construction	Wilson HS Pool/Nat	Jacquelyn Roberts	7	5/20/21	5/12/22				
Owner Move-in	Wilson HS Pool/Nat	Jacquelyn Roberts	7	5/13/22	5/26/22				
<b>Phase: 8</b>									
<b>Project Name: Carver ES Modernization</b>									
Construction	Carver ES Modernization	Leslie Sydnor	8	5/17/23	5/8/24				
Owner Move-in	Carver ES Modernization	Leslie Sydnor	8	5/9/24	5/22/24				
<b>Project Name: Franklin MS Track/Field</b>									
Construction	Franklin MS Track/Field	Brooke Clements	8	1/18/24	9/18/24				
Owner Move-in	Franklin MS Track/Field	Brooke Clements	8	9/19/24	9/19/24				
<b>Project Name: Henry ES HVAC</b>									
Construction	Henry ES HVAC	James Fortunes	8	8/28/23	8/23/24				
Owner Move-in - Phase 1	Henry ES HVAC	James Fortunes	8	3/10/24	3/22/24				
Owner Move-in - Phase 2	Henry ES HVAC	James Fortunes	8	8/26/24	9/6/24				
<b>Project Name: Lindberg MS Track/Field</b>									
Construction	Lindberg MS Track/Field	Tracy Nishihira	8	7/10/23	3/8/24				
Owner Move-in	Lindberg MS Track/Field	Tracy Nishihira	8	7/10/23	7/21/23				
<b>Project Name: Marshall MS Track/Field</b>									
Construction	Marshall MS Track/Field	Leslie Sydnor	8	1/25/24	9/25/24				
Owner Move-in	Marshall MS Track/Field	Leslie Sydnor	8	9/26/24	10/9/24				
<b>Project Name: Millikan HS Pool/Nat</b>									
Construction	Millikan HS Pool/Nat	Leslie Sydnor	8	5/23/23	7/15/24				
Owner Move-in	Millikan HS Pool/Nat	Leslie Sydnor	8	7/16/24	7/29/24				
<b>Phase: 9</b>									
<b>Project Name: Poly HS Pool/Nat</b>									
Construction	Poly HS Pool/Nat	Brooke Clements	9	9/2/24	9/19/25				
Owner Move-in	Poly HS Pool/Nat	Brooke Clements	9	9/22/25	10/3/25				
<b>Phase: 10</b>									
<b>Project Name: Buffum TK HVAC</b>									
Construction	Buffum TK HVAC	Jacquelyn Roberts	10	6/18/25	6/10/26				
Owner Move-in	Buffum TK HVAC	Jacquelyn Roberts	10	6/11/26	6/24/26				
<b>Project Name: Hudson K-8 Track/Field</b>									
Construction	Hudson K-8 Track/Field	Elston Soares	10	6/5/25	11/5/25				
Owner Move-in	Hudson K-8 Track/Field	Elston Soares	10	11/6/25	11/19/25				
<b>Project Name: Monroe MOD</b>									
Construction	Monroe MOD	James Fortunes	10	12/11/25	8/12/26				
Owner Move-in	Monroe MOD	James Fortunes	10	8/13/26	8/26/26				
<b>Project Name: Powell K8 Track/Field</b>									
Construction	Powell K8 Track/Field	Tracy Nishihira	10	4/11/25	8/8/25				
<b>Project Name: Tucker SpEd HVAC</b>									
Construction	Tucker SpEd HVAC	Jacquelyn Roberts	10	6/15/25	6/19/26				
Owner Move-in	Tucker SpEd HVAC	Jacquelyn Roberts	10	6/22/26	7/3/26				
<b>State: Complete</b>									
<b>Phase: 0FA</b>									
<b>Project Name: Fire Alarms/Life Safety Sys - Phase II</b>									
Construction	Fire Alarms/Life Safety Sys - Phase II	Alex Main	OFA	6/30/16	6/30/17				

Project updates      Task      Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE as of 5/31/2018**

Task Name	Project Name	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
<b>Phase: OSC</b>				<b>7/6/17</b>	<b>1/30/18</b>				
<b>Project Name: Security Camera Phase II</b>				<b>7/6/17</b>	<b>1/30/18</b>				
Construction	Security Camera Phase II	Mickey Kim	OSC	7/6/17	1/30/18				
<b>Phase: 1</b>				<b>1/6/15</b>	<b>3/6/18</b>				
<b>Project Name: Cabrillo HS Track/Field</b>				<b>6/15/17</b>	<b>11/28/17</b>				
Construction	Cabrillo HS Track/Field	James Warmuth	1	6/15/17	10/26/17				
Owner Move-in	Cabrillo HS Track/Field	James Warmuth	1	11/14/17	11/28/17				
<b>Project Name: Monroe K8 Interim Housing</b>				<b>7/21/17</b>	<b>12/26/17</b>				
Construction	Monroe K8 Interim Housing	Raymond Esparza	1	7/21/17	12/11/17				
Owner Move-in	Monroe K8 Interim Housing	Raymond Esparza	1	12/22/17	12/26/17				
<b>Project Name: Poly HS Auditorium</b>				<b>1/6/15</b>	<b>11/2/17</b>				
Construction	Poly HS Auditorium	Dan Barr	1	1/6/15	10/26/17				
Owner Move-in	Poly HS Auditorium	Dan Barr	1	10/23/17	11/2/17				
<b>Project Name: Poly HS Band Bldg Conversion Work</b>				<b>10/23/17</b>	<b>11/16/17</b>				
Construction	Poly HS Band Bldg Conversion Work	Dan Barr	1	10/23/17	11/14/17				
Owner Move-in	Poly HS Band Bldg Conversion Work	Dan Barr	1	11/15/17	11/16/17				
<b>Project Name: Riley ES Interim Housing</b>				<b>10/20/17</b>	<b>12/28/17</b>				
Construction	Riley ES Interim Housing	Raymond Esparza	1	10/20/17	12/22/17				
Owner Move-in	Riley ES Interim Housing	Raymond Esparza	1	12/27/17	12/28/17				
<b>Project Name: Rogers MS Portables</b>				<b>10/16/17</b>	<b>12/31/17</b>				
Construction	Rogers MS Portables	Richard Camacho	1	10/16/17	12/7/17				
Owner Move-in	Rogers MS Portables	Richard Camacho	1	12/29/17	12/31/17				
<b>Project Name: Sato HS Conversion</b>				<b>6/5/17</b>	<b>9/8/17</b>				
Construction	Sato HS Conversion	Richard Camacho	1	6/5/17	9/8/17				
Owner Move-in	Sato HS Conversion	Richard Camacho	1	8/1/17	8/18/17				
<b>Project Name: Sato HS Gym</b>				<b>5/23/16</b>	<b>1/31/18</b>				
Construction	Sato HS Gym	Richard Camacho	1	5/23/16	1/31/18				
Owner Move-in	Sato HS Gym	Richard Camacho	1	8/21/17	1/8/18				
<b>Project Name: Wilson HS Auditorium</b>				<b>2/22/16</b>	<b>3/6/18</b>				
Construction	Wilson HS Auditorium	Richard Camacho	1	2/22/16	2/19/18				
Owner Move-in	Wilson HS Auditorium	Richard Camacho	1	2/21/18	3/6/18				

Project updates      Task      Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.
