







Long Beach Unified School District Citizen's Oversight Committee

Quarterly Financial Update on Measure K Bond Program



June 24, 2010



June 24, 2010

Mr. Victor McCarty Chair, Measure K Bond Citizens' Oversight Committee c/o Long Beach Unified School District 2425 Webster Avenue Long Beach, CA 90810

Re: Quarterly Financial Update on Measure K Bond Program

Dear Mr. McCarty,

We are pleased to provide the Citizens' Oversight Committee with the quarterly financial update which includes the Master Program Budget report and individual project budget reports for the Long Beach Unified School District Measure K Bond Program.

As indicated on the enclosed reports, current budgets reflect known conditions through May 31, 2010, and expenditures through April 30, 2010.

We look forward to reviewing the reports with the committee on the evening of June 24th, and answering any questions you might have at that time.

Sincerely,

Tim Doane

Tim Doane Budget and Accounting Manager Capital Program Management, Inc.



Long Beach Unified School District Executive Summary June 24, 2010

Program Balance previously published on 04-01-2010		\$	0		
Funding Changes					
Increased Measure A funding associated with amendments to existing Measure A contracts and project specific Measure A expenditures transferred from the General Fund:					
- New 6-8 Middle School #1 (GTE)	51,005				
- New High School #1 (ECATS)	5,326				
Decrease Measure A funding to reflect coding corrections on the New					
6-8 Middle School #1 (GTE) project	(467,003)				
Total Funding Changes (Decreased Program Balance)		(41)),672)		
Budget Increases Increased Budget to cover additional expenditures incurred and for anticipated additional expenditures for fiscal year 2010-2011					
- New 6-8 Middle School #1 (GTE)	(705,815)				
- New High School #1 (ECATS)	(169,802)				
- Measure K Program Expenses	(60,000)				
Budget decreases					
Decreased the budget allocation for Future Projects - Unassigned.	1,346,289				
Total Net Budget Decreases (Increased Program Balance)		410	0,672		
Decreased the budget allocation for Future Projects - Unassigned. 1,346,289 Total Net Budget Decreases (Increased Program Balance) Program Balance after budget modifications					

Note: Total Measure K Expenditures to Date = \$61,314,703


I. Master Program Budget




Fiscal Period	State School Facilities Program	Measure K General Obligation Bond	Measure K Debt Retirement	Measure A General Obligation Bond	Interest Earnings	Other
Prior Fiscal Years				4,395,096		
Fiscal Year 2008-2009		260,000,000	(51,250,000)	3,342,566	585,220	
Fiscal Year 2009-2010	19,951,160			6,394,572	1,500,000	
Fiscal Year 2010-2011				365,221	3,000,000	
Fiscal Year 2011-2012		235,000,000		17,500	2,500,000	
Fiscal Year 2012-2013				17,500	4,500,000	
Fiscal Year 2013-2014		235,000,000			2,600,000	
Fiscal Year 2014-2015					4,300,000	
Fiscal Year 2015-2016		235,000,000			2,500,000	
Fiscal Year 2016-2017					4,500,000	
Fiscal Year 2017-2018		235,000,000			3,200,000	
\$ 1,212,4	18,835 \$ 19,951,160	\$ 1,200,000,000	\$ (51,250,000)	\$ 14,532,455	\$ 29,185,220	\$-

	BUDGETS through 05/31/10 & EXPENDITURES through 04/30/10										
Project		ninary dget	Current Budget		Committed Contracts		ensed Date	Percentage Complete			
Current Projects											
New 6-8 Middle School #1 (GTE Site)		53,261,715	54,422,	561	47,403,374		15,011,968	28%			
New High School #1 (ECATS)	1	00,325,055	100,650,	944	5,925,808		4,532,321	5%			
Future Projects											
Unassigned Projects	5	578,951,230	579,170,	947	-		-	0%			
District Wide Projects (Various Sites)											
Unassigned Projects	1	70,000,000	170,000,	000	-		-	0%			
									_		
Project Subtotal	\$9	02,538,000	\$ 904,244,	452	\$ <u>53,329,182</u>	\$	19,544,289	2%	_		
Measure K Program Expenses		29,930,000	30,059,	383	14,872,917		1,892,296	6%			
Construction Cost Escalation	2	251,021,000	251,039,	000							
Loss Reserve		27,076,000	27,076,	000							
Program Expenses / Reserves	\$ 3	08,027,000	\$ 308,174,	<mark>383</mark>							
Program Balance	\$	-	\$	-							
Program Totals	\$ 1,2	10,565,000	\$ 1,212,418,	835	\$ 68,202,099	\$	21,436,585	2%			

MASTER PROGRAM BUDGET June 24, 2010

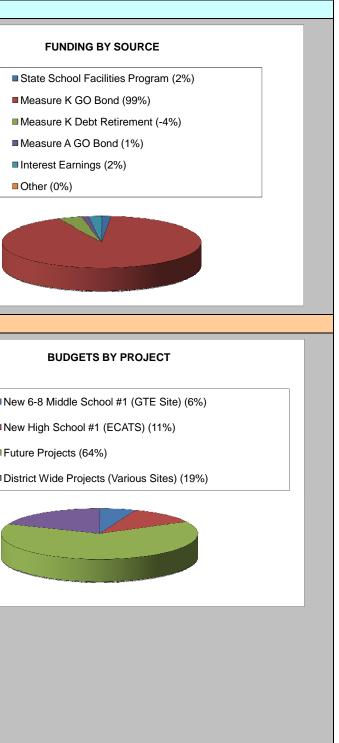






	Program Balance										
Date	Amount	To/From	Reason								
	-										
11/30/09	515,977	Program Balance	Increase Program Balance - Increase Measure A funding to cover project specific Measure A expenditures transferred from the General Fund for fiscal year 08/09								
11/30/09	95,141	Program Balance	Increase Program Balance - Increase Measure A funding to cover amendments to existing Measure A contracts for the New High School #1 (ECATS) project and the expenditure adjustment for the New 6-8 Middle School #1(GTE Site) project.								
11/30/09	1,470,251	Program Balance	Increase Program Balance - Increase Measure A funding to reflect the reallocation of existing expenditures and contract balances from Measure K to Measure A								
11/30/09	(188,930)	New High School #1 (ECATS)	Decrease Program Balance - Measure A funding transferred to New High School #1 (ECATS)								
11/30/09	(1,173,021)	New 6-8 Middle School #1(GTE)	Decrease Program Balance - Measure A funding transferred to New 6-8 Middle School #1 (GTE Site)								
11/30/09	(719,418)	Program Expenses	Decrease Program Balance - Measure A funding transferred to Program Expenses								
11/30/09	32,843	New High School #1 (ECATS)	Increase Program Balance - Transferred from project to reflect reallocation of expenditures and contract balances from Measure K to Measure A								
11/30/09	717,990	New 6-8 Middle School #1(GTE)	Increase Program Balance - Transferred from project to reflect reallocation of expenditures and contract balances from Measure K to Measure A								
11/30/09	719,418	Measure K Program Expenses	Increase Program Balance - Transferred from project to reflect reallocation of expenditures and contract balances from Measure K to Measure A								
11/30/09	(1,452,251)	Future Projects- Unassigned	Decrease Program Balance - Increase budget allocation for future projects								
	(/ - / - /										
11/30/09	(18,000)	Construction Cost Escalation	Decrease Program Balance - Increase escalation due to increased budget allocation for future projects								
	· · · · ·		Increase Program Balance - Increase Measure A funding to cover amendments to existing Measure A contracts and project								
02/26/10	87,007	Program Balance	specific Measure A expenditures transferred from the General Fund for the New 6-8 Middle School #1 (GTE Site) project								
	- /		Increase Program Balance - Increase Measure A funding to cover amendments to existing Measure A contracts and project								
02/26/10	96,131	Program Balance	specific Measure A expenditures transferred from the General Fund for the New High School #1 (ECATS)								
02/26/10	(87,007)	New 6-8 Middle School #1(GTE)	Decrease Program Balance - Measure A funding transferred to New 6-8 Middle School #1 (GTE Site)								
02/26/10	(96,131)	New High School #1 (ECATS)	Decrease Program Balance - Measure A funding transferred to New High School #1 (ECATS)								
02/26/10	87,007	New 6-8 Middle School #1(GTE)	Increase Program Balance - Transferred from project to reflect reallocation of funding due to increased funding from Measure A								
02/26/10	96,131	New High School #1 (ECATS)	Increase Program Balance - Transferred from project to reflect reallocation of funding due to increased funding from Measure A								
02/26/10	(69,383)	Measure K Program Expenses	Decrease Program Balance - Transferred to project due to cost of improvements to Measure K bond office, including procurement of furniture and equipment								
02/26/10	(113,755)	Future Projects- Unassigned	Decrease Program Balance - Increase budget allocation for future projects								
03/31/10	51,005	Program Balance	Increase Program Balance - Increase Measure A funding to cover amendments to existing Measure A contracts and project specific Measure A expenditures transferred from the General Fund for the New 6-8 Middle School #1 (GTE Site) project								
03/31/10	(467,003)	Program Balance	Decrease Measure A funding to reflect coding corrections, reallocating committed contracts and expenditures to Measure K on the New 6-8 Middle School #1 (GTE) project								
			Increase Program Balance - Increase Measure A funding to cover project specific Measure A expenditures transferred from the								
03/31/10	521	Program Balance	General Fund for the New High School #1 (ECATS)								
03/31/10	(51,005)	New 6-8 Middle School #1(GTE)	Decrease Program Balance - Measure A funding transferred to New 6-8 Middle School #1 (GTE Site)								
03/31/10	467,003	New 6-8 Middle School #1(GTE)	Increase Program Balance - Measure A funding transferred from New 6-8 Middle School #1 (GTE Site)								
03/31/10	(521)	New High School #1 (ECATS)	Decrease Program Balance - Measure A funding transferred to New High School #1 (ECATS)								
03/31/10	51,005	New 6-8 Middle School #1(GTE)	Increase Program Balance - Transferred from project to reflect reallocation of funding due to increased funding from Measure A								
03/31/10	(467,003)	New 6-8 Middle School #1(GTE)	Decrease Program Balance - Transferred to project to reflect reallocation of funding due to decreased funding from Measure A								
03/31/10	521	New High School #1 (ECATS)	Increase Program Balance - Transferred from project to reflect reallocation of funding due to increased funding from Measure A								
03/31/10	(665,745)	New 6-8 Middle School #1(GTE)	Decrease Program Balance - Transferred to project due to anticipated expenditures for fiscal year 2010-2011								
03/31/10	(143,402)	New High School #1 (ECATS)	Decrease Program Balance - Transferred to project due to anticipated expenditures for fiscal year 2010-2011								
03/31/10	1,224,624	Future Projects- Unassigned	Increase Program Balance - Decrease budget allocation for future projects								

BUILDING ON SUCCESS - SCHOOLS FOR THE NEXT GENERATION

M



			Program Balance
Date	Amount	To/From	Reason
04/30/10	(40,070)		Decrease Program Balance - Transferred to project due to anticipated expenditures for fiscal year 2010-2011
04/30/10	40,070	Future Projects- Unassigned	Increase Program Balance - Decrease budget allocation for future projects
			Increase Program Balance - Increase Measure A funding to cover project specific Measure A expenditures transferred from the
05/31/10	4,805	Program Balance	General Fund for the New High School #1 (ECATS)
05/31/10	(4,805)		Decrease Program Balance - Measure A funding transferred to New High School #1 (ECATS)
05/31/10	4,805	New High School #1 (ECATS)	Increase Program Balance - Transferred from project to reflect reallocation of funding due to increased funding from Measure A
			Decrease Program Balance - Transferred to project due to estimated costs for Printing & Distribution, Advertising & Notices, and
05/31/10	(60,000)	Measure K Program Expenses	Escrow/Title Fees
05/31/10	(26,400)	New High School #1 (ECATS)	Decrease Program Balance - Transferred to project due to anticipated expenditures for fiscal year 2010-2011
05/31/10	81,595	Future Projects- Unassigned	Increase Program Balance - Decrease budget allocation for future projects
Balance:	\$-		

BUILDING ON SUCCESS - SCHOOLS FOR THE NEXT GENERATION

TT.



MASTER PROGRAM BUDGET - ESCALATION/LOSS RESERVE June 24, 2010

			Construction Cost Escalation
Date	Amount	To/From	Reason
	251,021,000		Per Escalation Calculation
11/30/09	18,000	Program Balance	Increase escalation due to increased budget allocation for future projects
Balance:	\$ 251,039,000		
			Loss Reserve
Date	Amount	To/From	Reason
	27,076,000		3% of total project budgets
	A		
Balance:	\$ 27,076,000		

II. Program Expenses



BUDGET SUMMARY REPORT

Meas	ure K Program Expens	es					Complexity simplified.	
	FU	NDING			В	UDGET SUMMARY		
	Source	Original Amount	Funding Modifications	Current Amount				
Measur	e K General Obligation Bonds	29,760,125	(590,035)	29,170,090			I	
Measur	e A General Obligation Bonds	169,875	719,418	889,293	District Facilities (0%)	■Consultants	; (98%)	
Interest	Earnings	-	-					
Other		_	_	_	Bond Development & Ov	versight (2%) □Maintenanc	e & Operations (0%)	
					Debt Service Retirement	t (0%) Other (0%)		
	TOTAL FUNDING:	\$ 29,930,000	\$ 129,383	\$ 30,059,383				
	BUDGETS tl	nrough 05/31	I/10		EXPEND	ITURES through	04/30/10	
Code	Description	Preliminary Budget	Budget Modifications	Current Budget	Committed Contracts	Expensed To Date	Balance Remaining	
А	District Facilities	-	-	-	-	-	-	
В	Consultants	29,430,000	60,000	29,490,000	14,807,777	1,886,577	12,921,20	
С	Bond Development & Oversight	500,000	69,383	569,383	65,140	5,719	59,42	
D	Maintenance & Operations	-	-		-	-	-	
Е	Debt Service Retirement	-	-		-		-	
F	Other							
	Loss Reserve	-	-	-				
	Escalation	-	-	•				
	Contingency	-	-	-				
	Division Subtotal	\$-	\$ - !	\$-				



FUNDING DETAIL

Measu	ire K Program Expenses								q	Complexity simplified	
	FUNDING	SUMMARY									
	Source	Original Amount	Funding Modifications	Current Amount	FUNDING SUMMARY						
Measure K	General Obligation Bonds										
State R	Required Match		-	-							
Addition	nal Allocation	29,760,125	(590,035)	29,170,090							
Program	m Balance		-	-			tang dan di sa	CONTRACTOR DE LA CONTRACTOR DE LA CONTRACTÓR DE CONTRACTÓR DE LA CONTRACTÓ			
Constru	uction Cost Escalation		-	-							
Loss Re	eserve		-	-		Мореци	e K General	Obligation Bon	de (07%)		
Tota		29,760,125	(590,035)	29,170,090			e n General	Congation Dom			
	General Obligation Bonds	169,875	719,418	889,293		■Measu	e A General	Obligation Bon	ds (3%)		
nterest Ear	rnings		-	-				-			
Other			-	-		Interest	t Earnings (09	%)			
			-	-		□Other (0%)				
			-	-			0 %)				
	Totals	\$ 29,930,000	. ,	\$ 30,059,383							
		FU	JNDING M	ODIFICATIO	DNS						
			Measur	Measure K General Obligation Bonds Measure A							
Date	Description	State Required Match	Additional Allocation	Program Balance	Construction Cost Escalation	Loss Reserve	Total	General Obligation Bonds	Interest Earnings	Other	
	Funding adjustment to reflect reallocation of										
11/30/09	expenditures and contract balances from										
	Measure K to Measure A		(719,418)				(719,418)	719,418			
	Increase Measure K funding due to										
02/26/10	improvements to Measure K Bond Office,										
02/20/10	including procurement of furniture and										
	equipment		69,383				69,383				
	Increase Measure K funding due to estimated										
	Miscellaneous Consultant Costs for Printing &										
05/31/10	Distribution, Advertising & Notices, and										
00/01/10	Escrow/Title Fees. Commitments and										
	expenses will be reallocated as project costs										
	are identified.		60,000				60,000				
							-				
							-				
							-				
							-				
							-				
		•					-	• -··			
	Totals	\$ -	\$ (590,035)	¢ _	\$ -	\$ -	\$(590,035)	\$ 719,418	\$ -	\$	



BUDGET MODIFICATIONS PROCESSED DURING CURRENT PERIOD

Measure K Program Expenses

BUDGET MODIFICATIONS FOR THE CURRENT REPORTING PERIOD

From: 03/01/10 To: 05/31/10

com.

Total Budget Prior to Modifications: \$ 29,999,383

Code	Date	Number	Amount	Reason for Modification
oouc	Dute	Rumber	Amount	Increase Miscellaneous Consultant Costs due to estimated costs for Printing & Distribution, Advertising & Notices, and Escrow/
020.02120	05/31/10	2	60,000	Fees. Commitments and expenses will be reallocated as project costs are identified.
			,	
		Total:	60,000	
otal Budget	Following Mo	difications:	\$ 30,059,383	



Measure	e K Program Expenses								(complexity simplified.	
			BUDGET		COMMITMENTS				EXPENDITURES		
Code	Budget Description	Preliminary Budget	Budget Modifications	Current Budget	Original Contract	Approved Changes	Pending Changes	Current Commitment	Expensed To Date	Balance Remaining	
Α	District Facilities										
010.01010	Assistant Superintendent	-	-	-	-	-	-	-	-	-	
010.01020	Director	-	-	-	-	-	-	-	-	-	
010.01030	Assistant Director	-	-	-	-	-	-	-	-	-	
010.01040	Project Managers	-	-	-	-	-	-	-	-	-	
010.01050	Construction Coordinators	-	-	-	-	-	-	-	-	-	
010.01060	Construction Technicians	-	-	-	-	-	-	-	-	-	
010.01070	Accountants	-	-	-	-	-	-	-	-	-	
010.01080	Administrative Assistants	-	-	-	-	-	-	-	-	-	
010.01090	Planners	-	-	-	-	-	-	-	-	-	
010.01100	Modernization Coordinator	-	-	-	-	-	-	-	-	-	
	Division Subtotal	\$-	\$ -	\$-	\$-	\$-	\$-	\$-	\$-	\$-	
		-									
В	Consultants										
020.02010	Planning	-	-		-	-	-	-	-		
020.02020	Program Management	22,500,000	-	22,500,000	13,343,871	562.800	-	13,906,671	1.639.076	12,267,595	
020.02030	Budget Tracking & Reporting	2,250,000	-	2,250,000	889,293	-	-	889,293	238,127	651,167	
020.02040	Contract Administration	-	-	-	-	-	-	-	-	-	
020.02050	Prevailing Wage Compliance	-	-		-	-	-	-	-		
020.02060	Design Standards	-	-		-	-	-	-	-		
020.02070	Quality Assurance Control	2,250,000	-	2,250,000	-	-	-	-	-		
020.02080	Legal Fees	2,200,000	-	2,200,000	-	-	-	-	-		
020.02090	Auditor	180,000	-	180,000	11,000	-	-	11,000	8,561	2,439	
020.02030	CEQA	100,000	-	100,000	-	_	-	-	-		
020.02100	Eligibility	2,250,000	-	2,250,000		_	-	-	-		
020.02110	Miscellaneous Consultant Costs	2,200,000	60,000	60,000	813	-	-	813	813		
020.02120	Division Subtotal	\$ 29,430,000	\$ 60,000	\$ 29,490,000	\$ 14,244,977	\$ 562,800	\$ -	\$ 14,807,777	\$ 1,886,577	\$ 12,921,200	
	Bittolon Cubicital	φ 20,100,000	φ 00,000	φ 20,100,000	φ 11,211,011	φ 002,000	Ψ	φ 11,007,777	φ 1,000,011	φ 12,021,200	
С	Bond Development & Oversight										
030.03010	Election Costs		-		-	-	-	-	-	-	
030.03010	Public Relations	500,000	-	500,000	-	-				-	
030.03020	Admin Fees	500,000		500,000	-	-				-	
030.03030	Bond Issuance Cost			-	-	-				-	
030.03040	Bond Office		69,383	- 69,383	- 65,140	-	-	- 65,140		59,420	
030.03050	Division Subtotal	\$ 500.000	,	\$ 569.383	\$ 65,140		<u>-</u> \$ -	\$ 65,140		,	
	Division Sublota	φ 300,000	ψ 09,303	ψ 009,303	φ 05,140	φ -	Ψ -	φ 05,140	φ 5,719	φ 59,420	
D	Maintenance & Operations							+	+	+	
040.04010	M&O Budget Encroachment	-	-	-	-	-	-	-	-	-	
040.04020	Maintenance Reserve	-	-	-	-	-	-	-	-	-	
	Division Subtotal	\$-	\$-	\$-	\$-	\$-	\$-	\$-	\$-	\$-	



			BUDGET			COMMI	TMENTS		EXPEN	DITURES
Code	Budget Description	Preliminary Budget	Budget Modifications	Current Budget	Original Contract	Approved Changes	Pending Changes	Current Commitment	Expensed To Date	Balance Remaining
Е	Debt Service Retirement									
050.05010	Payoff COP's	-	-	-	-	-	-	-	-	-
050.05020	Bridge Financing Costs	-	-	-	-	-	-	-	-	-
050.05030	Bond Debt Payment	-	-	-	-	-	-	-	-	-
	Division Subtotal	\$-	\$-	\$-	\$-	\$-	\$-	\$-	\$-	\$-
F	Other									
090.09010	Loss Reserve	-	-	-						
090.09020	Escalation	-	-	-						
090.09030	Contingency	-		-						
	Division Subtotal	\$-	\$-	\$-	1					
	TOTAL	\$ 29,930,000	\$ 129,383	\$ 30,059,383	\$ 14,310,117	\$ 562,800	\$-	\$ 14,872,917	\$ 1,892,296	\$ 12,980,621

III. New 6-8 Middle School #1 (GTE Site)



BUDGET SUMMARY REPORT

New 6-8 Middle School #1 (GTE Site) FUNDING											
Measure K General Obligation Bonds	33,364,909	316,816	33,681,725								
Measure A General Obligation Bonds	6,993,084	844,030	7,837,114	■Site							
Interest Earnings	-	-	-	□Cons							
State School Facilities Program	12,903,722	-	12,903,722	Cons							
Career Technical Education	-	-	-	■Furni ■Conti							
TOTAL FUNDING:	\$ 53,261,715	\$ 1,160,846	\$ 54,422,561								

BUDGETS through 05/31/10

Code	Description	F	Preliminary Budget	Budget Modifications	Current Budget	Committed Contracts
А	Site Costs		4,837,693	41,870	4,879,563	4,
В	District and Agency Costs		301,960	95,460	397,420	
С	Consultant Costs		3,216,519	1,098,539	4,315,058	3,
D	Bid Costs		-	15,584	15,584	
Е	Construction Costs		38,542,281	(40,000)	38,502,281	38,
F	Construction Support Costs		1,195,400	-	1,195,400	1,
G	Furniture & Equipment Costs		2,317,428	-	2,317,428	
Н	Miscellaneous Project Costs		-	-	-	
Ι	Contingencies					
	Construction Contingency		108,195	-	108,195	
	Project Contingency		811,085	(50,607)	760,478	
	Owner Contingency		1,931,154	-	1,931,154	
	Division Subtotal	\$	2,850,434	\$ (50,607)	\$ 2,799,827	
		_				
TOTA	AL ESTIMATED PROJECT COST:	\$	53,261,715	\$ 1,160,846	\$ 54,422,561	\$ 47,

OPSC #: 53/647	25-00-002
BUDGET SUM	MARY
Site Costs (9%)	District and Agency Costs (1%)
Consultant Costs (8%)	□Bid Costs (0%)
Construction Costs (71%)	Construction Support Costs (2%)
Furniture & Equipment Costs (4%)	Miscellaneous Project Costs (0%)
Contingencies (5%)	

EXPENDITURES through 04/30/10

Committed Contracts	Expensed To Date	Balance Remaining
4,124,562	3,555,731	568,831
375,357	338,764	36,592
3,199,356	2,601,624	597,732
6,418	6,418	-
38,502,281	8,202,333	30,299,948
1,195,400	307,096	888,304
-	<u> </u>	-
-	-	-
\$ 47,403,374 \$	15,011,968	\$ 32,391,406



FUNDING DETAIL

	FUNDING S	SUMMARY									
	Source	Original Amount	Funding Modifications	Current Amount			FUNDI	NG SUMM	ARY		
Measure K	General Obligation Bonds	Amount	woullications	Amount							
	guired Match	12,903,722	-	12,903,722							
	I Allocation	20,461,187	316,816	20,778,003				-			
Program	Balance		-	-			1000		Togle.		
	tion Cost Escalation		-	-							
Loss Res	erve		-	-	■Mea	sure K General C	bligation Bonds (62	2%) ■Meas	sure A Genera	Obligation Bonds (14%)
Total		33,364,909	316,816	33,681,725							
	General Obligation Bonds	6,993,084	844,030	7,837,114	□Inter	est Earnings (0%)	■State	e School Facilit	ies Program (24%)	
nterest Ea			-	-							
	ol Facilities Program	12,903,722	-	12,903,722	Care	er Technical Edu	cation (0%)				
Jareer Tec	hnical Education	* 50 004 745		-							
	Totals	\$ 53,261,715	. , ,	. , ,							
			FUNDIN	g Modifia	CATIONS						
			Measur	e K General Obl	igation Bonds			Measure A General	Interest	State School	Career
Date	Description	State Required Match	Additional Allocation	Program Balance	Construction Cost Escalation	Loss Reserve	Total	Obligation Bonds	Earnings	Facilities Program	Technica Educatior
	Increase Measure A funding to cover project										
11/30/09	specific Measure A expenditures transferred from										
	the General Fund for fiscal year 08/09						-	455,031			
44/00/00	Funding adjustment to reflect reallocation of										
11/30/09	expenditures and contract balances from Measure K to Measure A		(717.990)				(717,990)	717,990			
	Reallocation of funding due to increased funding		(717,990)				(717,990)	717,990			
	from Measure A associated with amendments to										
02/26/10	existing Measure A contracts and project specific										
02/20/10	Measure A expenditures transferred from the										
	General Fund		(87,007)				(87,007)	87,007			
	Reallocation of funding due to increased funding							,			
	from Measure A associated with amendments to										
	existing Measure A contracts and project specific										
	Measure A expenditures transferred from the										
03/31/10	General Fund		(51,005)				(51,005)	51,005			
	Reallocation of funding due to decreased funding										
	from Measure A associated with a refund received										
	from State Water Resources Control and coding corrections for DSA fees and Environmental										
03/31/10	Services		467,003				467,003	(467,003)			
00/01/10			407,003				407,003	(407,003)			
03/31/10	Increase funding due to anticipated additional expenditures for fiscal year 2010-2011		665,745				665,745				
	Increase funding due to additional expenditures		000,745				005,745				
00/01/10											
			40.070				10 070				
04/30/10	incurred for hazardous waste removal		40,070				40,070				
			40,070				40,070				



BUDGET MODIFICATIONS PROCESSED DURING CURRENT PERIOD

GET MOD	IFICATIONS F	OR THE CURI		G PERIOD From: 03/01/10 To: 05/31/10
Total Budg	get Prior to Mo	difications:	\$ 53,716,746	
Code	Date	Number	Amount	Reason for Modification
260.007	03/31/10	3	3,600	Increase Fees - Gas due to project specific Measure A expenditure transfers from the General Fund anticipated in fiscal year 2010/201
999.096	03/31/10	3	(3,600)	
260.070	03/31/10	3	10,000	Increase Printing & Distribution due to project specific expenditure transfers from the General Fund anticipated in fiscal year 2010/2011
260.040	03/31/10	3	655,745	Increase Legal Services due to project specific expenditure transfers from the General Fund anticipated in fiscal year 2010/2011
175.090	04/30/10	4	40,070	Increase Environmental-Other due to State Board of Equalization fees paid for hazardous waste removal (this is a Measure A contract)
260.080	04/30/10	4	164	Increase Advertisements & Notices due to project specific Measure A expenditures transferred from the General Fund
260.070	04/30/10	4	(164)	Decrease Printing & Distribution to fund Advertisements & Notices
		Total	705,815	



									EXPENDITURES		
			BUDGET			COMMI	MENTS		EXPEND	ITURES	
	Budget Description	Preliminary Budget	Budget Modifications	Current Budget	Original Contract	Approved Changes	Pending Changes	Current Commitment	Expensed To Date	Balance Remaining	
Α	Site Costs	0		Ŭ			0				
6110.000	Site Acquisition	-	-	-	-	-	-	-	-	-	
6120.000	Property Appraisal	9,600	-	9,600	10,500	(900)	-	9,600	9,600	-	
6130.000	Escrow/Title Fees	-	-	-	-	-	-	-	-	-	
6140.000	Site Surveys	-	-	-	-	-	-	-	-	-	
	CEQA Reports and Other Studies	123,993	-	123,993	123,993	-	-	123,993	123,993	-	
6150.001	CEQA	103,593	-	103,593	103,593	-	-	103,593	103,593		
6150.002	Traffic Engineering Study	-	-	-	-	_	-	-	-		
6150.003	Geotechnical Study	20,400	-	20,400	20,400	-	-	20,400	20,400		
6150.004	Geohazard Study	-	-	-	-	-	-	-	-		
6150.090	Other Site Studies	-	-		-	-		_	-		
0100.000	Environmental	-	40,070	40,070	40,070	-		40,070	40,070		
6175.001	Environmental - Phase 1	-	-	-	-	-	-	-	-		
6175.002	Environmental - Phase 2	-	-	-	-	-	-	-	-		
6175.003	Environmental - PEA	-		-	-			_	-		
6175.004	Environmental - RAW	-	-	-	-		_	-	-		
6175.004	Environmental - EMS						<u>-</u>				
6175.005	Environmental - Pipeline	-	-	-	-	-	-	-	-		
6175.006	Environmental - Pipeline Environmental - Railroad			-	-		-	-	-		
				-	-		-	-			
6175.008	Environmental - Aeronautical	-							-		
6175.090	Environmental - Other	-	40,070	40,070	40,070	-	-	40,070	40,070		
6185.000	Environmental - Clean Up / Remediation	4,668,672	-	4,668,672	3,990,324	(76,652)	-	3,913,672	3,344,841	568,	
6176.000	Other Costs - Site	35,428	1,800	37,228	37,227	-	-	37,227	37,227		
	Division Subtotal	\$ 4,837,693	\$ 41,870	\$ 4,879,563	\$ 4,202,114	\$ (77,552)	\$-	\$ 4,124,562	\$ 3,555,731	\$ 568,	
В	District and Agency Costs										
6220.000	Fees - DSA	100,150	90,092	190.242	190,242	-	-	190,242	190.242		
6230.000	Fees - CDE	21,879	-	21,879	21,878		-	21,878	21,878		
6175.040	Environmental - DTSC Fees	164,106	-	164,106	11,624	133,693		145,317	108,725	36,	
6240.000	Energy Analysis Fee	-	-	-	1	133,093			,	30,	
6250.000	Preliminary Tests	-		-	-	-	-	-	-		
6250.000	Other Costs - Utilities		1.000	-			-	1.000			
0074 004			1	1,000	1,000			1	1,000		
6274.001	Utility Set-Up Fees - Gas	-	-	-	-	-		-	-		
6274.002	Utility Set-Up Fees - Electrical	-		-	-			-	-		
6274.003	Utility Set-Up Fees - Water	-	-	-	-	-	-	-	-		
6274.004	Utility Set-Up Fees - Sewer	-	-	-	-	-	-	-	-		
6274.005	Utility Set-Up Fees - Storm Drainage	-	-	-	-	-	-	-	-		
6274.006	Utility Set-Up Fees - Telephone	-	-	-	-	-	-	-	-		
6274.007	Utility Set-Up Fees - Cable TV	-	1,000	1,000	1,000	-	-	1,000	1,000		
	Other Costs - Agency Fees	15,825	4,368	20,193	17,172	(253)	-	16,919	16,919		
6260.001	Fees - CHPS	-	-	-	-	-	-	-	-		
6260.002	Fees - CGS	-	-	-	-	-	-	-	-		
6260.003	Fees - AQMD	-	-	-	-	-	-	-	-		
6260.004	Fees - Health Department	1,213	-	1,213	1,213	-	-	1,213	1,213		
6260.005	Fees - Industrial Waste	-	-	-	-	-	-	-	-		
6260.006	Fees - SWPP	-	-	-	-	-	-	-	-		
6260.007	Fees - Gas	10,400	4,368	14,768	11,747	-	-	11,747	11,747		
6260.008	Fees - Electrical	-	-	-	-	-	-	-	-		



			BUDGET			COMMI	MENTS		EXPEND	ITURES
	Budget	Preliminary	Budget	Current	Original	Approved	Pending	Current	Expensed	Balance
	Description	Budget	Modifications	Budget	Contract	Changes	Changes	Commitment	To Date	Remaining
6260.010	Fees - Sewer	-	-	-	-	-	-	-	-	-
6260.011	Fees - Storm Drainage	777	-	777	777	-	-	777	777	-
6260.012	Fees - Telephone	-	-	-	-	-	-	-	-	-
6260.013	Fees - Cable Television	-	-	-	-	-	-	-	-	-
6260.014	Fees - Other Agencies	3,435	-	3,435	3,435	(253)	-	3,182	3,182	-
	Division Subtotal	\$ 301,960	\$ 95,460	\$ 397,420	\$ 241,916	\$ 133,440	\$ -	\$ 375,357	338,764	\$ 36,592
0	Concultant Conta									
С	Consultant Costs									
6210.000	Architect / Engineering Fees	3,112,844	-	3,112,844	3,076,196	-	-	3,076,196	2,497,964	578,232
6260.021	Eligibility Consultant	-	-	-	-	-	-	-	-	-
6260.022	CHPS Consultant	-	-		-	-	-	-	-	-
6260.023	Estimating Consultant	22,675	-	22,675	28,100	(5,425)	-	22,675	22,675	-
6260.024	Constructability Review	-	-	-	-	-	-	-	-	-
6260.025	Legislative Consultant	-	-	-	-	-	-	-	-	-
6260.030	Project Management	-	-	-	-	-	-	-	-	-
6260.040	Legal Services	-	1,098,539	1,098,539	442,794	(382,808)	-	59,985	59,985	-
6260.050	Low Voltage Design	-		-	-		-	-	-	-
6260.060	Community Outreach	-	-	-	-	-	-	-	-	-
6175.051	HazMat Design	-	-	-	-	-	-	-	-	-
6175.052	HazMat Monitoring			-	-	-	-	-	-	-
6277.000	Labor Compliance	81,000	-	81,000	81,000	(40,500)	-	40,500	21,000	19,500
6260.090	Other Consultant Costs	-	=	-	-	- (400 700)		-	-	-
	Division Subtotal	\$ 3,216,519	\$ 1,098,539	\$ 4,315,058	\$ 3,628,089	\$ (428,733)	\$-	\$ 3,199,356	\$ 2,601,624	\$ 597,732
<u> </u>	Did Casta									
D	Bid Costs									
6260.070	Printing & Distribution	-	15,420	15,420	6,255	-	-	6,255	6,255	-
6260.080	Advertisements & Notices	-	164	164	163	-	-	163	163	-
	Division Subtotal	\$-	\$ 15,584	\$ 15,584	\$ 6,418	\$ -	\$ -	\$ 6,418	\$ 6,418	\$-
Е	Construction Costs									
6180.000	Site Contractor	-	-	-	-	-		-	-	-
6260.035	Pre-Construction Services	260,150	(40,000)	- 220,150	260,150	(40,000)	-	220,150	220,150	-
0200.035	Main Construction Contractor	38,282,131	(40,000)	38,282,131	38,282,131	(40,000)		38,282,131	7,982,183	30,299,948
6270.000	Main Construction Contractor Main Contractor - General Contractor	-	-	-	-	-	-	-	7,962,163	- 30,299,940
6270.000	Main Contractor - Ceneral Contractor Main Contractor - L/LB - Lease	-			-			-	-	-
6270.021	Main Contractor - L/LB - Contract	38,282,131		38,282,131	38,282,131			38,282,131	7,982,183	30,299,948
6270.022	Main Contractor - D/LB - Contract	- 30,202,131	-	- 30,202,131	- 30,202,131	-			7,962,163	30,299,940
6270.030	Main Contractor - Low Voltage	-		-	-			-		
6270.071	Main Contractor - Pathway			-	-	-	-	-		
6270.071	Main Contractor - Fire Alarm	-	-	-	-			-	-	
6270.072	Main Contractor - File Alarm Main Contractor - Assistive Listening	-	-		-	-		-	-	
6270.073	Main Contractor - Assistive Listening Main Contractor - Data	-	-		-	-		-		
6270.074	Main Contractor - Data Main Contractor - Telephone	-	-	-	-	-	-	-	-	
6270.075	Main Contractor - Telephone Main Contractor - Intercom	-	-		-	-	-	-		
6270.076	Main Contractor - Intercom Main Contractor - Clocks and Bells	-	-		-	-		-		
6270.077	Main Contractor - Clocks and Bells Main Contractor - Intrusion	-	-		-			-		
6270.078	Main Contractor - Intrusion Main Contractor - Cable TV	-	-		-	-		-	-	-
6270.079	Main Contractor - Cable 1 V Main Contractor - EMS	-	-	-	-	-		-		
		-	-	-	-	-	-	-	-	-
6270.081 6270.082	Main Contractor - Digital Video Security					-	-			
	Main Contractor - Video Media Demolition - Existing Features	-	-	-	-	-	-	-	-	-
6273.000 6274.050	Owner Furnished Materials	-	-	-	-	-	-	-	-	-
0214.000	Owner Fullished Materials	-	-	-	-	-	-	-	-	-



			BUDGET			COMMI	TMENTS			DITURES
	Budget	Preliminary	Budget	Current	Original	Approved	Pending	Current	Expensed	Balance
	Description	Budget	Modifications	Budget	Contract	Changes	Changes	Commitment	To Date	Remaining
6274.090	Other Costs - Construction	-	-	-	-	-	-	-	-	-
	Relocatable Buildings	-	-	-	-	-	-	-	-	-
6275.001	Relocatable - Purchase Costs	-	-	-	-	-	-	-	-	-
6275.002	Relocatable - Lease Costs	-	-	-	-	-	-	-	-	-
6275.003	Relocatable - Install/Move/Other	-	-	-	-	-	-	-	-	-
	Division Subtotal	\$ 38,542,281	\$ (40,000) \$ 38,502,281	\$ 38,542,281	\$ (40,000)	\$-	\$ 38,502,281	\$ 8,202,333	\$ 30,299,94
_										
F	Construction Support Costs									
6290.000	Construction Inspection	712,000	-	712,000		-	-	712,000	109,458	602,54
6280.000	Construction Testing	404,400	-	404,400		-	-	404,400	118,638	285,76
6272.000	Construction Manager	79,000	-	79,000	79,000	-	-	79,000	79,000	-
6274.060	Security for Construction Site	-	-	-	-	-	-	-	-	-
6274.070	Systems Start-Up / Training	-	-	-	-	-	-	-	-	-
	Division Subtotal	\$ 1,195,400	\$-	\$ 1,195,400	\$ 1,195,400	\$-	\$-	\$ 1,195,400	\$ 307,096	\$ 888,30
-										
G	Furniture & Equipment Costs									
4310.000	F&E-Supplies (under \$500)	-	-	-	-	-	-	-	-	-
	F&E - (\$500-\$5000)	2,317,428	-	2,317,428		-	-	-	-	-
4400.000	F&E-Non-Tech (\$500-\$5000)	2,317,428	-	2,317,428		-	-	-	-	-
4400.010	F&E-Tech (\$500-\$5000)	-	-	-	-	-	-	-	-	-
6310.000	Books & Media for New Libraries	-	-	-	-	-	-	-	-	-
	F&E-Capitalized - (over \$5000)	-	-	-	-	-	-	-	-	-
6490.000	F&E-Capitalized - Non-Tech (over \$5000)	-	-	-	-	-	-	-	-	-
6490.010	F&E-Capitalized - Tech (over \$5000)	-	-	-	-	-	-	-	-	-
	Division Subtotal	\$ 2,317,428	\$-	\$ 2,317,428	\$-	\$ -	\$-	\$ -	\$ -	\$-
н	Miscellaneous Project Costs									
	Interim Housing	-	-		-	_	-		_	
6276.002	Interim Housing - Lease Costs	-	-	-	-	-	-	-	-	-
6276.002	Interim Housing - Lease Costs	-	-	-	-	-	-	-	-	-
6274.080	Move/Store for Construction	-		-				-		-
0214.000	Division Subtotal	\$-	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
			-							
I	Contingencies									
6999.095	Construction Contingency	108,195	-	108,195						
6999.096	Project Contingency	811,085	(50,607) 760,478						
6999.097	Owner Contingency	1,931,154	-	1,931,154]					
	Division Subtotal	\$ 2,850,434	\$ (50,607	\$ 2,799,827						
	TOTAL	\$ 53,261,715	\$ 1,160,846	\$ 54,422,561	\$ 47,816,218	\$ (412,844)	¢	\$ 47,403,374	\$ 15,011,968	\$ 32,391,40

IV. New High School #1 (ECATS)



BUDGET SUMMARY REPORT

	High School #1 (ECAT	S)			0	PSC #: 50/64725-00-000	0 CCOM.
	FL	JNDING				BUDGET SUMMA	RY
	Source	Original Amount	Funding Modifications	Current Amount			
Measur	e K General Obligation Bonds	87,761,956	35,502	87,797,458			
Measur	e A General Obligation Bonds	5,515,661	290,387	5,806,048	Site Costs (0%)	District and	d Agency Costs (1%)
	Earnings				Consultant Costs (5%)	■Bid Costs	• • • •
		7.047.400		7.047.400	■Construction Costs (75%)	Constructi	ion Support Costs (1%)
	chool Facilities Program	7,047,438	-	7,047,438	Furniture & Equipment Costs	(5%) Miscellane	eous Project Costs (0%)
Career	Technical Education	-	-	-	Contingencies (14%)		
	TOTAL FUNDING:	\$ 100,325,055	\$ 325,889	\$ 100,650,944			
	BUDGETS	through 05/31	I/10		EXPENDIT	URES through 0	04/30/10
Code	Description	Preliminary Budget	Budget Modifications	Current Budaet	Committed Contracts	Expensed To Date	Balance Remaining
Code A	Description Site Costs	Preliminary Budget 181,096	Budget Modifications 211,346	Current Budget 392,442	Committed Contracts 305,145	Expensed To Date 266,139	Balance Remaining 39
	-	Budget	Modifications	Budget	Contracts	To Date	Remaining
A	Site Costs	Budget 181,096	Modifications 211,346	Budget 392,442	Contracts 305,145	To Date 266,139	Remaining 39
A B	Site Costs District and Agency Costs Consultant Costs	Budget 181,096 639,800	Modifications 211,346 22,246	Budget 392,442 662,046	Contracts 305,145 447,246	To Date 266,139 438,578	Remaining 39
A B C D	Site Costs District and Agency Costs Consultant Costs Bid Costs	Budget 181,096 639,800 4,744,915 -	Modifications 211,346 22,246 136,001 19,187	Budget 392,442 662,046 4,880,916 19,187	Contracts 305,145 447,246 4,648,112 17,805	To Date 266,139 438,578 3,340,142 17,019	Remaining 39 8 1,307
A B C D E	Site Costs District and Agency Costs Consultant Costs Bid Costs Construction Costs	Budget 181,096 639,800 4,744,915 - 81,458,876	Modifications 211,346 22,246 136,001 19,187 (5,951,376)	Budget 392,442 662,046 4,880,916 19,187 75,507,500	Contracts 305,145 447,246 4,648,112	To Date 266,139 438,578 3,340,142	Remaining 39
A B C D E F	Site Costs District and Agency Costs Consultant Costs Bid Costs Construction Costs Construction Support Costs	Budget 181,096 639,800 4,744,915 - 81,458,876 750,000	Modifications 211,346 22,246 136,001 19,187	Budget 392,442 662,046 4,880,916 19,187 75,507,500 980,000	Contracts 305,145 447,246 4,648,112 17,805 507,500	To Date 266,139 438,578 3,340,142 17,019 470,443	Remaining 39 8 1,307
A B C D E F G	Site Costs District and Agency Costs Consultant Costs Bid Costs Construction Costs Construction Support Costs Furniture & Equipment Costs	Budget 181,096 639,800 4,744,915 - 81,458,876	Modifications 211,346 22,246 136,001 19,187 (5,951,376)	Budget 392,442 662,046 4,880,916 19,187 75,507,500	Contracts 305,145 447,246 4,648,112 17,805 507,500	To Date 266,139 438,578 3,340,142 17,019 470,443	Remaining 39 8 1,307
A B C D E F	Site Costs District and Agency Costs Consultant Costs Bid Costs Construction Costs Construction Support Costs Furniture & Equipment Costs Miscellaneous Project Costs	Budget 181,096 639,800 4,744,915 - 81,458,876 750,000	Modifications 211,346 22,246 136,001 19,187 (5,951,376) 230,000 -	Budget 392,442 662,046 4,880,916 19,187 75,507,500 980,000 4,550,000	Contracts 305,145 447,246 4,648,112 17,805 507,500 - -	To Date 266,139 438,578 3,340,142 17,019 470,443 - -	Remaining 39 8 1,307
A B C D E F G	Site Costs District and Agency Costs Consultant Costs Bid Costs Construction Costs Construction Support Costs Furniture & Equipment Costs Miscellaneous Project Costs Contingencies	Budget 181,096 639,800 4,744,915 - 81,458,876 750,000 4,550,000 -	Modifications 211,346 22,246 136,001 19,187 (5,951,376) 230,000 - -	Budget 392,442 662,046 4,880,916 19,187 75,507,500 980,000 4,550,000 -	Contracts 305,145 447,246 4,648,112 17,805 507,500 - -	To Date 266,139 438,578 3,340,142 17,019 470,443 - -	Remaining 39 8 1,307
A B C D E F G	Site Costs District and Agency Costs Consultant Costs Bid Costs Construction Costs Construction Support Costs Furniture & Equipment Costs Miscellaneous Project Costs	Budget 181,096 639,800 4,744,915 - 81,458,876 750,000	Modifications 211,346 22,246 136,001 19,187 (5,951,376) 230,000 -	Budget 392,442 662,046 4,880,916 19,187 75,507,500 980,000 4,550,000	Contracts 305,145 447,246 4,648,112 17,805 507,500 - -	To Date 266,139 438,578 3,340,142 17,019 470,443 - -	Remaining 39 8 1,307
A B C D E F G	Site Costs District and Agency Costs Consultant Costs Bid Costs Construction Costs Construction Support Costs Furniture & Equipment Costs Miscellaneous Project Costs Contingencies Construction Contingency	Budget 181,096 639,800 4,744,915	Modifications 211,346 22,246 136,001 19,187 (5,951,376) 230,000 - - 617,246	Budget 392,442 662,046 4,880,916 19,187 75,507,500 980,000 4,550,000 - 4,617,430	Contracts 305,145 447,246 4,648,112 17,805 507,500 - -	To Date 266,139 438,578 3,340,142 17,019 470,443 - -	Remaining 39 8 1,307



Г

FUNDING DETAIL

٦

	FUNDING SU	JMMARY									
	Source	Original Amount	Funding Modifications	Current Amount	1		FUNE	DING SUM	MARY		
Measure K	General Obligation Bonds	Amount	woullications	Anount	-						
	quired Match	7,047,438	-	7,047,438			\sim				
	al Allocation	80,714,518	35,502	80,750,020							
Program	Balance		-	-			Waters Of COLUMN		The second second		
Construc	tion Cost Escalation		-	-							
Loss Res	serve		-	-	D Mass		Obligation Bonds	(070/)		eral Obligation Bonds	(69()
Total		87,761,956	35,502	87,797,458	unieas	Sule K General	Obligation Bonds	(07%) U IVI	easure A Gene	Tai Obligation Bonds	(0%)
	General Obligation Bonds	5,515,661	290,387	5,806,048							
nterest Ea			-	-	□Intere	est Earnings (0	1%)	□St	ate School Fac	cilities Program (7%)	
	ol Facilities Program	7,047,438	-	7,047,438	_						
Career Tec	chnical Education		-	-	■Caree	er Technical E	ducation (0%)				
	Totals	\$ 100,325,055		\$ 100,650,944							
			FUNDIN		CATIONS						
			Measu	re K General Ob	ligation Bonds			Measure A	• • •	State School	Career
Date	Description	State Required Match	Additional Allocation	Program Balance	Construction Cost Escalation	Loss Reserve	Total	General Obligation Bonds	Interest Earnings	Facilities Program	Technica Educatio
	Increase Measure A funding to cover project							201140			
11/30/09	specific Measure A expenditures transferred from										
	the General Fund for fiscal year 08/09						-	67,096			
11/20/00	Increase Measure A funding due to contract amendments for Pre-Construction, Geotechnical										
11/30/09	Study, and CEQA							88,991			
	Funding adjustment to reflect reallocation of						-	00,991			
11/30/09	expenditures and contract balances from										
11/00/00	Measure K to Measure A		(32,843)				(32,843)	32,843			
	Reallocation of funding due to increased funding		(02,010)				(02,010)	02,010			
	from Measure A associated with amendments to										
02/26/10	existing Measure A contracts and project specific										
	Measure A expenditures transferred from the										
	General Fund		(96,131)				(96,131)	96,131			
	Reallocation of funding due to increased funding										
	from Measure A associated with project specific										
~~ /~ / / / ~	Measure A expenditures transferred from the		(50.0)				(== ()				
03/31/10	General Fund		(521)				(521)	521			
03/31/10	Increase funding due to anticipated additional expenditures for fiscal year 2010-2011		143,402				143,402				
03/31/10	Reallocation of funding due to increased funding		143,402				143,402				
	from Measure A associated with project specific										
	Measure A expenditures transferred from the										
05/31/10	General Fund		(4,805)				(4,805)	4,805			
	Increase funding due to anticipated additional		(1,500)				(1,000)	.,500			
05/31/10	expenditures for fiscal year 2010-2011		26,400				26,400				
			.,				-				
							-				
	Totals		\$ 35,502		\$-	\$ -	\$ 35,502	\$ 290,387	\$-	\$-	\$



BUDGET MODIFICATIONS PROCESSED DURING CURRENT PERIOD

New High School #1 (ECATS)

OPSC #: 50/64725-00-000

From: 03/01/10 To: 05/31/10

cpm.

BUDGET MODIFICATIONS FOR THE CURRENT REPORTING PERIOD

Total Budget Prior to Modifications: \$ 100,481,142

	_		-	
Code	Date	Number	Amount	Reason for Modification
6150.003	03/31/10	3	60,000	Increase Geotechnical Study due to budget re-evaluation for Geotechnical Study expenses anticipated in fiscal year 2010/2011
6175.003	03/31/10	3	35,000	Increase Environmental - PEA due to budget re-evaluation for Environmental - PEA expenses anticipated in fiscal year 2010/2011
6260.040	03/31/10	3	38,402	Increase Legal Services due to project specific expenditure transfers from the General Fund anticipated in fiscal year 2010/2011
6260.070	03/31/10	3	10,000	Increase Printing & Distribution due to project specific expenditure transfers from the General Fund anticipated in fiscal year 2010/207
6260.080	03/31/10	3	2,000	Increase Advertisements & Notices due to project specific expenditure transfers from the General Fund anticipated in fiscal year 2010/2011
6999.096	03/31/10	3	(2,000)	Decrease Project Contingency to fund Advertisements & Notices
6260.080	04/30/10	4	3,369	Increase Advertisements & Notices due to project specific Measure A expenditures transferred from the General Fund
6999.096	04/30/10	4	(3,369)	Decrease Project Contingency to fund Advertisements & Notices
6260.024	05/17/10	5	26,400	Increase Constructability Review due to anticipated costs associated with specification changes during plan check
		Total	169,802	
otal Budge	t Following Mo	difications:	\$ 100,650,944	



New High School #1 (ECATS)

OPSC #: 50/64725-00-000



			BUDGET			COMMITM	IENTS		EXPEND	ITURES
Code	Budget Description	Preliminary Budget	Budget Modifications	Current Budget	Original Contract	Approved Changes	Pending Changes	Current Commitment	Expensed To Date	Balance Remaining
Α	Site Costs	Budget	woullications	Бийдег	Contract	Changes	Changes	Communent	To Date	Remaining
6110.000	Site Acquisition	-	-	-	-	-	-	-	-	-
6120.000	Property Appraisal	-	-	-	-	-	-	-	-	-
6130.000	Escrow/Title Fees	-	-	-	-	-	-	-	-	
6140.000	Site Surveys	25,720	-	25,720	25,720	-	-	25,720	25,720	-
	CEQA Reports and Other Studies	150,776	141,591	292,367	149,575	90,496	-	240,071	201,065	39,0
6150.001	CEQA	51,556	19,596	71,152	51,555	19,596	-	71,151	39,386	31,
6150.002	Traffic Engineering Study	28,500	24,000	52,500	28,500	24,000	-	52,500	47,329	5,1
6150.003	Geotechnical Study	70,720	97,995	168,715	69,520	46,900	-	116,420	114,350	2,
6150.004	Geohazard Study	-	-	-	-	-	-	-	-	
6150.090	Other Site Studies	-	-	-	-	-	-	-	-	
	Environmental	4,600	35,000	39,600	4,600	-	-	4,600	4,600	
6175.001	Environmental - Phase 1	4,600	-	4,600	4,600	-	-	4,600	4,600	
6175.002	Environmental - Phase 2	-	-	-	-	-	-	-	-	
6175.003	Environmental - PEA	-	35,000	35,000	-	-	-	-	-	
6175.004	Environmental - RAW	-	-	-	-	-	-	-	-	
6175.005	Environmental - EMS	-	-	-	-	-	-	-	-	
6175.006	Environmental - Pipeline	-	-	-	-	-	-	-	-	
6175.007	Environmental - Railroad	-	-	-	-	-	_	-	-	
6175.008	Environmental - Aeronautical	-	-	-	-	-	-	-	-	
6175.090	Environmental - Other	-		-	-	-	_	-	_	
6185.000	Environmental - Clean Up / Remediation	-	-	-	-	-	-	-	-	
6176.000	Other Costs - Site		34,755	- 34,755	34,754	-		34,754	34,754	
0170.000	Division Subtotal	\$ 181.096	\$ 211.346 \$	392,442	\$ 214.649		-	\$ 305.145	\$ 266.139	\$ 39,
		φ 101,090	φ 211,340 φ	392,442	φ 214,049	φ 90,490 φ	-	φ 305,145	φ 200,139	φ 39,0
В	District and Agency Costs									
6220.000	Fees - DSA	402.100	_	402,100	402,100	-	-	402,100	402,100	
6230.000	Fees - CDE	- /		,	402,100	-	-	402,100	402,100	
6175.040	Fees - CDE									
6175.040	Environmental DTCC Fore	210,000	-	210,000	-		-	-	-	0
0040.000	Environmental - DTSC Fees	1,500	17,336	18,836	- 18,836	-	-	18,836	10,168	8,
6240.000	Energy Analysis Fee	1,500	17,336 -	18,836 -	-	-	-	18,836 -	10,168 -	8
6240.000 6250.000	Energy Analysis Fee Preliminary Tests	1,500 - -	17,336 - -	18,836 - -	-			18,836 - -	10,168 - -	8
6250.000	Energy Analysis Fee Preliminary Tests Other Costs - Utilities	1,500 - - -	17,336 - - -	18,836 - - -		- - - -		18,836 - - -	10,168 - - -	8
6250.000 6274.001	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas	1,500 - - - -	17,336 - - - - -	18,836 - - - - -	- - - -	- - - -	- - - -	18,836 - - - - -	10,168 - - - - -	8
6250.000 6274.001 6274.002	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical	1,500 - - -	17,336 - - -	18,836 - - -		- - - -		18,836 - - -	10,168 - - -	8
6250.000 6274.001 6274.002 6274.003	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Water	1,500 - - - -	17,336 - - - - -	18,836 - - - - -	- - - -	- - - -	- - - -	18,836 - - - - -	10,168 - - - - -	8
6250.000 6274.001 6274.002 6274.003 6274.004	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Water Utility Set-Up Fees - Sewer	1,500 	17,336 	18,836 - - - - - -	- - - - -		- - - - - -	18,836 - - - - - -	10,168 - - - - - -	8
6250.000 6274.001 6274.002 6274.003	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Water	1,500 - - - - - - - -	17,336 	18,836 - - - - - - - -	- - - - -		- - - - - - -	18,836 - - - - - - -	10,168 - - - - - - - - -	8
6250.000 6274.001 6274.002 6274.003 6274.004	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Sterr Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone	1,500 - - - - - - - - - -	17,336 	18,836 - - - - - - - - -	- - - - - -	- - - - - - - -	- - - - - - - - - -	18,836 - - - - - - - - - - - -	10,168 - - - - - - - - - -	8
6250.000 6274.001 6274.002 6274.003 6274.004 6274.005	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Vater Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone Utility Set-Up Fees - Cable TV	1,500 - - - - - - - - - - - - - - -	17,336 - - - - - - - - - - - - - - - - - -	18,836 - - - - - - - - - - - -	- - - - - - - - - - - -		- - - - - - - - - - - - - - -	18,836 - - - - - - - - - - - - -	10,168 - - - - - - - - - - -	8
6250.000 6274.001 6274.002 6274.003 6274.004 6274.005 6274.006	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Vater Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone Utility Set-Up Fees - Cable TV	1,500 - - - - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - -	- - - - - - - - - - - - -		- - - - - - - - - - - - - - - -	18,836 - - - - - - - - - - - - - -	10,168 - - - - - - - - - - - - - -	8
6250.000 6274.001 6274.002 6274.003 6274.004 6274.005 6274.006	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Sterr Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone	1,500 - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - - - - -	- - - - - - - - - - - - -		- - - - - - - - - - - - - - - - - - -	18,836 - - - - - - - - - - - - - - - - - - -	10,168 - - - - - - - - - - - - - - - - - - -	8
6250.000 6274.001 6274.002 6274.003 6274.004 6274.005 6274.006 6274.007	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Sewer Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone Utility Set-Up Fees - Cable TV Other Costs - Agency Fees	1,500 - - - - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - - - - - - -	- - - - - - - - - - - - - - - - - - -		- - - - - - - - - - - - - - - - - - -	18,836 	10,168 - - - - - - - - - - - - - - - - - - -	8
6250.000 6274.001 6274.003 6274.003 6274.004 6274.005 6274.006 6274.007 6260.001 6260.002	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Water Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone Utility Set-Up Fees - Cable TV Other Costs - Agency Fees Fees - CHPS	1,500 - - - - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - - - - - - -	- - - - - - - - - - - 26,310 900		- - - - - - - - - - - - - - - - - - -	18,836 	10,168 - - - - - - - - - - - - - - - - - - -	8
6250.000 6274.001 6274.003 6274.003 6274.004 6274.005 6274.006 6274.007 6260.001 6260.002 6260.003	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Vater Utility Set-Up Fees - Sewer Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Cable TV Other Costs - Agency Fees Fees - CHPS Fees - AQMD	1,500 - - - - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - - - - - - -	- - - - - - - - - - - - - - - - - - -		- - - - - - - - - - - - - - - - - - -	18,836 	10,168 	8
6250.000 6274.001 6274.002 6274.003 6274.004 6274.005 6274.005 6274.007 6260.001 6260.001 6260.002 6260.003 6260.004	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Vater Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone Utility Set-Up Fees - Cable TV Other Costs - Agency Fees Fees - CHPS Fees - AQMD Fees - Health Department	1,500 - - - - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - - - - - - -			- - - - - - - - - - - - - - - - - - -	18,836 	10,168 - - - - - - - - - - - - - - - - - - -	8
6250.000 6274.001 6274.002 6274.003 6274.004 6274.005 6274.005 6274.007 6260.001 6260.001 6260.003 6260.004 6260.005	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone Utility Set-Up Fees - Cable TV Other Costs - Agency Fees Fees - CHPS Fees - AQMD Fees - Industrial Waste	1,500 - - - - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - - - - - - -				18,836 	10,168 	8
6250.000 6274.001 6274.002 6274.003 6274.004 6274.005 6274.006 6274.006 6274.007 6260.001 6260.002 6260.003 6260.005 6260.005 6260.006	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Water Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone Utility Set-Up Fees - Cable TV Other Costs - Agency Fees Fees - CGS Fees - Health Department Fees - Industrial Waste Fees - SWPP	1,500 - - - - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - - - - - - -	- - - - - - - - - - - - 26,310 900 3,600 - - 953 - - -		- - - - - - - - - - - - - - - - - - -	18,836 	10,168 - - - - - - - - - - - - - - - - - - -	8
6250.000 6274.001 6274.002 6274.003 6274.004 6274.005 6274.005 6274.007 6260.001 6260.003 6260.003 6260.004 6260.005	Energy Analysis Fee Preliminary Tests Other Costs - Utilities Utility Set-Up Fees - Gas Utility Set-Up Fees - Electrical Utility Set-Up Fees - Sewer Utility Set-Up Fees - Storm Drainage Utility Set-Up Fees - Telephone Utility Set-Up Fees - Cable TV Other Costs - Agency Fees Fees - CHPS Fees - AQMD Fees - Industrial Waste	1,500 - - - - - - - - - - - - - - - - - -	17,336 	18,836 - - - - - - - - - - - - - - - - - - -			- - - - - - - - - - - - - - - - - - -	18,836 	10,168 	8



		BUDGET			COMMITMENTS				EXPENDITURES		
Code	Budget	Preliminary	Budget	Current	Original	Approved	Pending	Current	Expensed	Balance	
	Description	Budget	Modifications	Budget	Contract	Changes	Changes	Commitment	To Date	Remaining	
6260.010	Fees - Sewer	-	-	-	-	-	-	-	-	-	
6260.011	Fees - Storm Drainage	-	-	-	-	-	-	-	-	-	
6260.012	Fees - Telephone	-	-	-	-	-	-	-	-	-	
6260.013	Fees - Cable Television	-	-	-	-	-	-	-	-	-	
6260.014	Fees - Other Agencies	-	357	357	357	-	-	357	357	-	
	Division Subtotal	\$ 639,800	\$ 22,246	\$ 662,046	\$ 447,246	\$-	\$-	\$ 447,246	\$ 438,578	\$ 8,668	
	O an and the set of a set of										
С	Consultant Costs										
6210.000	Architect / Engineering Fees	4,379,117	-	4,379,117	4,379,117	-	-	4,379,117	3,071,648	1,307,469	
6260.021	Eligibility Consultant	-	-	-	-	-	-	-	-		
6260.022	CHPS Consultant		-	-	-	-	-		-		
6260.023	Estimating Consultant	95,500	-	95,500	95,500	-	-	95,500	95,000	500	
6260.024	Constructability Review	80,000	26,260	106,260	79,860	-	-	79,860	79,860	-	
6260.025 6260.030	Legislative Consultant	-	-	-	-	-	-	-	-	-	
	Project Management	-	-	-	-	-	-	-	-	-	
6260.040	Legal Services	-	109,741	109,741	71,337	-	-	71,337	71,337	-	
6260.050	Low Voltage Design	-		-	-		-	-	-	-	
6260.060	Community Outreach	-	-	-	-	-	-	-	-	-	
6175.051	HazMat Design	22,298	-	22,298	22,297	-	-	22,297	22,297	<u> </u>	
6175.052 6277.000	HazMat Monitoring	128,000		128,000		-				-	
	Labor Compliance	40,000	-	40,000	-	-	-	-	-		
6260.090	Other Consultant Costs	-		-	-				-		
	Division Subtotal	\$ 4,744,915	\$ 136,001	\$ 4,880,916	\$ 4,648,112	\$ -	\$-	\$ 4,648,112	\$ 3,340,142	\$ 1,307,969	
D	Bid Costs										
-			10.000	10.000	44.004			44.004	44.004		
6260.070	Printing & Distribution	-	13,263	13,263	11,881	-	-	11,881	11,881	-	
6260.080	Advertisements & Notices Division Subtotal		5,924 \$ 19,187	5,924 \$ 19,187	5,924 \$ 17,805	- \$-	- \$-	5,924 \$ 17,805	5,137 \$ 17,019	786 \$ 786	
	Division Subtotal	р -	φ 19,107	\$ 19,107	φ 17,005	р -	ф -	φ 17,605	φ 17,019	φ /00	
Е	Construction Costs										
6180.000	Site Contractor	-	-	_	_	-	_	-		-	
6260.035	Pre-Construction Services	446,230	61,270	507,500	446,230	61,270	-	507,500	470,443	37,057	
0200.000	Main Construction Contractor	81,012,646	(6,012,646)	75,000,000	-	01,210	-		110,110	01,001	
6270.000	Main Contractor - General Contractor	-	(0,012,040)	-	-	-	-	-	-	-	
6270.021	Main Contractor - L/LB - Lease	-	-	-	-	-	-	-	-	-	
6270.022	Main Contractor - L/LB - Contract	81,012,646	(6,012,646)	75,000,000	-	-	-	-	-	-	
6270.050	Main Contractor - Multiple Prime	-	-	-	-	-	-	-	-	-	
6270.070	Main Contractor - Low Voltage	-	-	-	-	-	-	-	-	-	
6270.071								-	-	-	
	Main Contractor - Pathway	-	-	-	-	-	-				
	Main Contractor - Pathway Main Contractor - Fire Alarm	-	-	-	-	-	-	-	-	-	
6270.072	Main Contractor - Fire Alarm							-	-	-	
	Main Contractor - Pathway Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data	-	-	-	-	-	-				
6270.072 6270.073 6270.074	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data	-	-	-	-	-	-	-	-	-	
6270.072 6270.073 6270.074 6270.075	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data Main Contractor - Telephone							-	-	-	
6270.072 6270.073 6270.074	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data	- - - -	- - - -	- - - -	- - -	- - - -	- - - -		- - -	-	
6270.072 6270.073 6270.074 6270.075 6270.076 6270.077	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data Main Contractor - Telephone Main Contractor - Intercom Main Contractor - Clocks and Bells			- - - -	- - - -	- - - - -	- - - -	- - - -	- - - -	- - -	
6270.072 6270.073 6270.074 6270.075 6270.076 6270.077 6270.078	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data Main Contractor - Telephone Main Contractor - Intercom Main Contractor - Clocks and Bells Main Contractor - Intrusion	- - - - - - -	- - - - - -	- - - - - -	- - - - -	- - - - - -	- - - - - - -	- - - -	- - - - -	- - - - -	
6270.072 6270.073 6270.074 6270.075 6270.076 6270.077 6270.078 6270.079	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data Main Contractor - Telephone Main Contractor - Intercom Main Contractor - Clocks and Bells Main Contractor - Intrusion Main Contractor - Cable TV	- - - - - - -	- - - - - - -	- - - - - - - -	- - - - - -	- - - - - - - -	- - - - - - - - -	- - - - - -	- - - - -	- - - - - -	
6270.072 6270.073 6270.074 6270.075 6270.076 6270.077 6270.078 6270.079 6270.079	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data Main Contractor - Telephone Main Contractor - Intercom Main Contractor - Clocks and Bells Main Contractor - Intrusion Main Contractor - Cable TV Main Contractor - EMS	- - - - - - - - - - - -	- - - - - - - - - - -	- - - - - - - - - - -	- - - - - - - - - - - -	- - - - - - - - -	- - - - - - - - - - -	- - - - - - -	- - - - - -	- - - - - - - -	
6270.072 6270.073 6270.074 6270.075 6270.076 6270.077 6270.078 6270.079 6270.080 6270.081	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data Main Contractor - Telephone Main Contractor - Intercom Main Contractor - Intercom Main Contractor - Intercom Main Contractor - Intrusion Main Contractor - Cable TV Main Contractor - EMS Main Contractor - Digital Video Security	- - - - - - - - - - - - - - - -	- - - - - - - - - - - - - - - - -		- - - - - - - - - - - - - -	- - - - - - - - - - - -	- - - - - - - - - - - - - - - - - - -	- - - - - - - - - - - - - - -	- - - - - - - - - - - - -	- - - - - - - - - - -	
6270.072 6270.073 6270.074 6270.075 6270.076 6270.077 6270.078 6270.079 6270.079	Main Contractor - Fire Alarm Main Contractor - Assistive Listening Main Contractor - Data Main Contractor - Telephone Main Contractor - Intercom Main Contractor - Clocks and Bells Main Contractor - Intrusion Main Contractor - Cable TV Main Contractor - EMS	- - - - - - - - - - - - - -	- - - - - - - - - - - -		- - - - - - - - - - - -	- - - - - - - - - - - - - -	- - - - - - - - - - - - - - - - -	- - - - - - - - -	- - - - - - - - - - -	- - - - - - - - -	



		BUDGET				COMMI	TMENTS		EXPENDITURES	
Code	Budget	Preliminary	Budget	Current	Original	Approved	Pending	Current	Expensed	Balance
Code	Description	Budget	Modifications	Budget	Contract	Changes	Changes	Commitment	To Date	Remaining
6274.090	Other Costs - Construction	-	-	-	-	-	-	-	-	-
	Relocatable Buildings	-	-	-	-	-	-	-	-	-
6275.001	Relocatable - Purchase Costs	-	-	-	-	-	-	-	-	-
6275.002	Relocatable - Lease Costs	-	-	-	-	-	-	-	-	-
6275.003	Relocatable - Install/Move/Other	-	-	-	-	-	-	-	-	-
	Division Subtotal	\$ 81,458,876	\$ (5,951,376)	\$ 75,507,500	\$ 446,230	\$ 61,270	\$-	\$ 507,500	\$ 470,443	\$ 37,057
	O material O marked O at a									
F	Construction Support Costs									
6290.000	Construction Inspection	500,000	-	500,000	-	-	-	-	-	-
6280.000	Construction Testing	250,000	-	250,000	-	-	-	-	-	-
6272.000	Construction Manager	-	-	-	-	-	-	-	-	-
6274.060	Security for Construction Site	-	-	-	-	-	-	-	-	-
6274.070	Systems Start-Up / Training	-	230,000	230,000	-	-	-	-	-	-
	Division Subtotal	\$ 750,000	\$ 230,000	\$ 980,000	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
G	Furniture & Equipment Costs									
4310.000	F&E-Supplies (under \$500)	_		_		-		_		-
4310.000	F&E - (\$500-\$5000)	4,550,000	-		-		-		-	
1100.000		, ,	-	4,550,000	-	-	-	-	-	-
4400.000	F&E-Non-Tech (\$500-\$5000)	4,550,000	-	4,550,000	-	-	-	-	-	-
4400.010	F&E-Tech (\$500-\$5000)	-	-	-	-	-	-	-	-	-
6310.000	Books & Media for New Libraries	-	-	-	-	-	-	-	-	-
	F&E-Capitalized - (over \$5000)	-	-	-	-	-	-	-	-	-
6490.000	F&E-Capitalized - Non-Tech (over \$5000)	-	-	-	-	-	-	-	-	-
6490.010	F&E-Capitalized - Tech (over \$5000)	-	-	-	-	-	-	-	-	-
	Division Subtotal	\$ 4,550,000	\$-	\$ 4,550,000	\$-	\$-	\$ -	\$ -	\$ -	\$ -
н	Miscellaneous Project Costs									
	Interim Housing			-	-	-	-	-	-	-
6276.002	Interim Housing - Lease Costs	-		-	-	-	-	-	-	-
6276.002	Interim Housing - Lease Costs	-		-	-	-	-		-	-
6274.080	Move/Store for Construction	-	-	-	-		-	-		_
0274.080	Division Subtotal	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
	Contingencies									
6999.095	Construction Contingency	4,000,184	617,246	4,617,430						
6999.096	Project Contingency	4,000,184	(354,161)	3,646,023	1					
6999.097	Owner Contingency	-	5,395,400	5,395,400	1					
	Division Subtotal	\$ 8,000,368			1					
	TOTAL	\$ 100,325,055	\$ 325,880	\$ 100,650,944	\$ 5,774,042	\$ 151,766	\$.	\$ 5,925,808	\$ 4,532,321	\$ 1,393,48



